

OWNERSHIP CERTIFICATE

To Whom It May Concern

This is to certify that the following equipment listed below is the sole property of Sudhir Equipment Rental Company:

Equipment	AWP
Brand / Make	DINGLI
Asset ID	SD14SL-1484
Model Number	JCPT1418RT
Serial Number	JPR0024C00331
Working Height	14 Meter
Type	Diesel Scissor lift
Manufacturing Year	2024

This certification is issued to confirm the ownership status of the aforementioned equipment. Sudhir Equipment Rental Company holds full legal ownership rights over the listed equipment and retains all associated benefits and responsibilities. Should there be any queries or requests for verification regarding the ownership of the mentioned equipment, please do not hesitate to contact us at : Info@sudhirrentals.com

Sincerely,

Ajay Koul
General Manager
Sudhir Equipment Rental Company





بروج للتأمين التعاوني
Buruj Cooperative Insurance

شهادة التأمين - CERTIFICATE OF INSURANCE

Policy Holder Name	:	Sudhir Equipment Rental Company	:	اسم حامل الوثيقة
Policy Number	:	01/CPM/ 2025/000002	:	رقم الوثيقة
Policy Period	:	05/04/ 2025 to 04/04/2026	:	فترة الوثيقة
Description of Machinery / Equipment	:	DINGLI-AWPS-JCPT1418RT	:	وصف المعدة/ال لة
Chassis / Serial No.	:	JPR0024C00331	:	رقم الهيكل/ التسلسلي
Year of Manufacturing	:	2024	:	سنة الصنع
Asset ID No.	:	SD14SL-1484	:	رقم ال صل
Location	:	Kingdom of Saudi Arabia.	:	الموقع

BURUJ Cooperative Insurance Company certifies that above client is holding a Machinery/Equipment Insurance Policy for the above-mentioned Equipment in accordance with the above-mentioned Insurance Policy.

With effect from: 05/04/ 2025 to 04/04/2026

This Certificate has been issued upon Insured's request as per all terms and conditions, exclusions, warranties mentioned in the policy.

تشهد شركة بروج للتأمين التعاوني بأن السادة أعل ه مؤمنين لديها تأمين المكان/المعدات المذكورة أعل ه وذلك حسب وثيقة التأمين المذكورة أعل ه

والتي يبدأ تاريخ سريانها من ٢٠٢٥/٠٤/٠٥ إلى ٢٠٢٦/٠٤/٠٤

تم إصدار هذه الشهادة بناءً على طلب المؤمن له وذلك حسب الشروط وال استثناءات وال شتراطات المذكورة في الوثيقة.

Important Notices:

1. This Certificate does not pay any fines, penalties, bonds or cautions that may be imposed.
2. Original certificates are only accepted.
3. Due to the importance of correct information being stated in this certificate, kindly examine the document carefully and advise the Company of any difference.
4. In the event of changes in the above information, kindly contact +966-11-2938383

مل حظات هامة:

- ١) ل تطبق هذه الشهادة التأمين على الغرامات والعقوبات المالية بما في ذلك المخالفات أو الضمانات أو الكفالات التي قد تقرر.
- ٢) تقبل الشهادة ال صلية فقط.
- ٣) نظراً ل همية صحة البيانات الخاصة بكم في هذه الشهادة، الرجاء التأكد منها وإشعار الشركة في حالة وجود أي اختل فات.
- ٤) عند الحاجة إلى تعديل البيانات أعل ه يرجى ال اتصال على شركة بروج للتأمين التعاوني ٢٩٣٨٣٨٣-١١-٩٦٦+



BURUJ Cooperative Insurance Company

P.O. Box 51855, Riyadh 11553,

National Address 3385, Al Thomamah Road, An-Nada District.

800 124 0201 | burujinsurance.com

Issue Date: 3 April 2025



Sticker No.:
BV-3843

BUREAU VERITAS

Tel: +966 13 882 1071
Fax: +966 13 882 1072
Al Khobar, Saudi Arabia



BUREAU
VERITAS

EQUIP. S.N.: JPR 0024 Coo 331
EQUIP. NO.: SD14 SL - 1484
EQUIP. SWL: 363 KG
INSPECTION DATE: FEB 14, 2026
NEXT INSPECTION DATE: AUG 13, 2026
INSPECTOR NAME: M. M. M.
SAP #: 20019106

"S.A. INSPECTION DEPARTMENT APPROVED CONTRACTOR AGENCY"



SUDHIR

Service : 050 999 3274
Technician :

SD14 SL - 1484
Date: 23/11/2025
Present Service Hrs: 338
Next Service Hrs: 638
Technician: M. M. M.



Bureau Veritas, Saudi Arabia

8th Floor, Danah Business Tower, Olaya District, Al Khobar, Kingdom of Saudi Arabia

Tel No : +966 13 882 1071

Web : <https://middle-east.bureauveritas.com>



Report No.: 249184

LIFTING EQUIPMENT INSPECTION REPORT	RPO NO. N/A		CRM NO. -		Report No. 249184
	Area DAMMAM	Inspection Date 14/02/2026	Inspection Time 15:00	Previous Sticker	
				No.24-5362	Issue By BV
Department / Contractor SUDHIR EQUIPMENT RENTAL CO.	Equipment Number SD14SL-1484	Equipment Location BV		Inspection Result Pass	New Sticker No. BV-3843
Manufacturer DINGLI	Model JCPT1418RT	Capacity 363 KG	Type MEWP	Equipment Serial Number JPR0024C00331	Sticker Expiration Date 13/08/2026

Above Equipment was inspected by Bureau Veritas in accordance with applicable Saudi Aramco GI's, ASME and API Standards. Deficiencies that require corrective action are listed below. Specific repairs to correct each deficiency should be noted in the corrective action taken column.

No.	DEFICIENCIES / NOTES	Corrective Action Taken
1	-PERIODIC INSPECTION AND FUNCTION TEST FOR SELF-PROPELLED ELEVATING WORK PLATFORM AS PER AS S.ARAMCO GI 7.030 AND ANSI 92.6 -EQUIPMENT WAS FOUND SATISFACTORY AT THE TIME OF INSPECTION -FOLLOW PROPER PM REGULARLY	-

Receiver's Name : ARIF	Badge No : -	Technical Reviewer Name : MAHMOUD EL NAHAS Received Date: 14/02/2026	Inspector Name : MOHAMED OMARA
Telephone No: 055 222 8031	Receiver Signature : 	Signature: Reviewed Date: 14/02/2026 	Inspector's Signature : 

When re-inspection is requested, a complete copy of this report should be ready review by the inspector.

SAUDI ARAMCO INSPECTION CHECKLIST			SAIC NUMBER SAIC-U-7014		ISSUE DATE 12-Jan-23	DISCIPLINE ELEVATING/LIFTING EQUIPMENT	
SELF PROPELLED ELEVATING WORK PLATFORM							
PROJECT TITLE			WBS/BI/JO NUMBER		INSPECTION COMPANY Bureau Veritas, Saudi Arabia		
EQUIPMENT ID NUMBER : SD14SL-1484	EQUIPMENT DESCRIPTION/TYPE : MEWP		SERIAL NO. : JPR0024C00331		REPORT No.: 249184		
CAPACITY (SWL) : 363 KG	MANUFACTURER : DINGLI		FACILITY / LOCATION : BV				
REQUESTED INSPECTION DATE :	RFI No.	TASK COMPLETED DATE : 14/02/2026	EQUIPMENT OWNER : SUDHIR EQUIPMENT RENTAL CO.				

ACCEPTANCE CRITERIA

1. GENERAL REQUIREMENTS

		REFERENCE	PASS	FAIL	NA	REMARKS
1.1	Equipment documentation is available	ANSI/SAIA A92.5, G.I. 7.030	✓			
1.2	Previous inspection reports are checked	ANSI/SAIA A92.5, G.I. 7.030	✓			
1.3	Daily pre-operational inspection checklists are checked (if applicable)	ANSI/SAIA A92.6 Sec:7.6	✓			
1.4	Preventive Maintenance is established and updated records are maintained	ANSI/SAIA A92.6 Sec:7.6	✓			
1.5	Equipment is operated by a qualified operator	ANSI/SAIA A92.6	✓			
1.6	Warning notice, cautions or restrictions for safe operation and maintenance are clearly displayed and legible	ANSI/SAIA A92.6	✓			
1.7	A sign is posted warning the operator not to rely solely on any automatic device as a substitute for safe operating practice	G.I. 7.030	✓			

		REFERENCE	PASS	FAIL	NA	REMARKS
1.8	Manufacturer name, address, serial number and model are clearly marked or tagged	ANSI/SAIA A92.6	✓			
1.9	Safe working load and number of persons are clearly marked on the work platform	ANSI/SAIA A92.6, SAES-B067	✓			
1.10	Maximum platform height and reach are clearly marked	ANSI/SAIA A92.6	✓			
1.11	Maximum travel height and travel directions are clearly marked	ANSI/SAIA A92.6	✓			
1.12	Power rating are provided and marked (for AC and/or DC)	ANSI/SAIA A92.6	✓			
1.13	Platform and guardrails electrical insulation data are provided	ANSI/SAIA A92.6			✓	
1.14	Multiple configurations are described on the manual and the platform (if multiple ratings are used)	GI 7.030 Para: 5.1.2	✓			

2. INSPECTION POINTS

		REFERENCE	PASS	FAIL	NA	REMARKS
2.1	Platform surfaces are at least 18" (width & length) and are slip-resistent	ANSI/SAIA A92.6	✓			
2.2	Platform guardrails are provided and secure	ANSI/SAIA A92.6	✓			
2.3	Platform guardrails are 42" height (+/- 3")	ANSI/SAIA A92.6	✓			
2.4	Platform toeboard is fitted and at least 4" high	ANSI/SAIA A92.6	✓			
2.5	Moving parts are guarded	ANSI/SAIA A92.6	✓			
2.6	Access to the platform is provided	ANSI/SAIA A92.6	✓			
2.7	Access to the platform and gate inward opening with lock.	ANSI/SAIA A92.6 Sec: 4.12.4	✓			

		REFERENCE	PASS	FAIL	NA	REMARKS
2.8	Electrical cables, wiring and components are undamaged	ANSI/SAIA A92.6	✓			
2.9	Extendable axles function is satisfactory (where fitted)	ANSI/SAIA A92.6			✓	
2.10	Wheels and tyres are serviceable and undamaged	ANSI/SAIA A92.6	✓			
2.11	Safety harness anchorage is fitted in the platform	ANSI/SAIA A92.6	✓			
2.12	Platform controls operate the machine correctly	ANSI/SAIA A92.6	✓			
2.13	Platform controls are clearly marked with direction and mode of operation	ANSI/SAIA A92.6	✓			
2.14	Platform controls accessible to the operator	ANSI/SAIA A92.6	✓			
2.15	Platform controls return to "off" or "neutral" position when released	ANSI/SAIA A92.6	✓			
2.16	Platform controls are protected against inadvertent operation	ANSI/SAIA A92.6	✓			
2.17	Over-ride control for power functions is fitted at ground level control panel	ANSI/SAIA A92.6	✓			
2.18	Ground controls return to "off" or "neutral" position when released	ANSI/SAIA A92.6	✓			
2.19	Ground controls are clearly marked for direction and mode of operation	ANSI/SAIA A92.6	✓			
2.20	Ground controls do not include drive and steering functions	ANSI/SAIA A92.6	✓			
2.21	Ground controls are protected against inadvertent operation	ANSI/SAIA A92.6	✓			
2.22	Auxiliary (emergency) lowering, retracting and rotating controls are fitted and operable at platform control panel	ANSI/SAIA A92.6			✓	
2.23	Auxiliary (emergency) lowering, retracting and rotating controls are fitted and operable at ground control panel	ANSI/SAIA A92.6	✓			

		REFERENCE	PASS	FAIL	NA	REMARKS
2.24	Battery is secure, guarded and ventilated	ANSI/SAIA A92.6	✓			
2.25	Outrigger position microswitches and interlocks are fully functional at their control panel	ANSI/SAIA A92.6			✓	
2.26	Safety props or latches are installed for maintenance purposes (as prescribed by the manufacturer)	ANSI/SAIA A92.6	✓			
2.27	Air, Hydraulic and fuel systems are not leaking	ANSI/SAIA A92.6	✓			
2.28	Emergency stop button is available at ground control station	ANSI/SAIA A92.6	✓			
2.29	Emergency stop button is available at platform control station	ANSI/SAIA A92.6	✓			
2.30	There are no loose nuts, bolts, missing, worn or damaged parts around the structure	ANSI/SAIA A92.6	✓			
2.31	The equipment is free of defective and/or corroded members/joints	ANSI/SAIA A92.6	✓			
2.32	Working environment is hazard free and machine can be safely operated	ANSI/SAIA A92.6	✓			
2.33	An hour meter is fitted	ANSI/SAIA A92.6	✓			
2.34	A fire extinguisher is fitted (type depends on operating location)	ANSI/SAIA A92.6	✓			
2.35	All fluid levels for oil, water and hydraulic are adequate	ANSI/SAIA A92.6	✓			
2.36	All moving parts are lubricated	ANSI/SAIA A92.6	✓			
2.37	Emergency stop button is operable from platform station	ANSI/SAIA A92.6	✓			
2.38	Emergency stop button is operable from ground station	ANSI/SAIA A92.6	✓			
2.39	Lowering/retracting is operable from platform control	ANSI/SAIA A92.6	✓			

		REFERENCE	PASS	FAIL	NA	REMARKS
2.40	Lowering/retracting is operable from ground control	ANSI/SAIA A92.6	✓			
2.41	Raise/extend is operable from platform control	ANSI/SAIA A92.6	✓			
2.42	Boom raise/extend is operable from ground control	ANSI/SAIA A92.6	✓			
2.43	Fluid systems are leak-free with platform raised	ANSI/SAIA A92.6	✓			
2.44	Tilt alarm is operable (5 degrees out of level) (manually depress the edge of the tilt switch to cause alarm condition)	ANSI/SAIA A92.6	✓			
2.45	Tilt alarm is not combined with boom raise cut-out (dependent on machine manufacturer)	ANSI/SAIA A92.6	✓			
2.46	Steering is properly working when moving forward and in reverse directions	ANSI/SAIA A92.6	✓			
2.47	Brakes are in good working condition and can hold the machine on any slope (parking and moving)	ANSI/SAIA A92.6	✓			
2.48	Travel alarm is operable	ANSI/SAIA A92.6	✓			
2.49	Platform lowering alarm is operable	ANSI/SAIA A92.6	✓			
2.50	Machine is safely drivable from the platform when raised (fast, slow, forward and reverse modes)	ANSI/SAIA A92.6	✓			
2.51	The platform does not descend when in raised position and the power is off	ANSI/SAIA A92.6	✓			
2.52	Used ancillary equipment are in good condition, free of damages and do not create any hazardous condition (e.g. power sockets, extension cables and mechanical brackets)	ANSI/SAIA A92.6	✓			
2.53	Engine powered machines fuel lines are supported to minimize chafing	ANSI/SAIA A92.6	✓			
2.54	Engine powered machines fuel lines are positioned to minimize exposure to engine and exhaust heat	ANSI/SAIA A92.6	✓			

		REFERENCE	PASS	FAIL	NA	REMARKS
2.55	Engine powered machines exhaust system is provided with muffler	ANSI/SAIA A92.6	✓			

REMARKS

-

REFERENCE DOCUMENTS:

- 1- ANSI/SAIA A92.6 - 2006(R2014) Issue:Self - Propelled Elevating Work Platforms
- 2- SAES-B067 - 2020 Issue: Safety Identification and Safety Colors
- 3- SA GI 7.025-2018 Issue: Heavy Equipment Operator and Rigger Testing and Certification
- 4- SA GI 7.030 - 2023 Issue: Inspection and Testing Requirements for Elevating/Lifting Equipment

Signature

Inspected / Witnessed by 3rd Party Certified Inspector

Name MOHAMED OMARA

Signature

Certificate No. 80019106

Company Bureau Veritas

Telephone No 055 078 7628

User Representative

Name ARIF

Signature



Date 14/02/2026

Badge -

Telephone No: 055 222 8031



Sticker No:
BV-3843

Bureau Veritas

Tel.: + 966 013 822

1071

Fax: + 966 013 822

1072

Al Khobar, Saudi
Arabia



EQUIP .S.N: JPR0024C00331

EQUIP .NO : SD14SL-1484

EQUIP.SWL : 363 KG

INSPECTION DATE : 14/02/2026

NEXT INSPECTION DATE :13/08/2026

INSPECTOR NAME: MOHAMED OMARA

SAP # 80019106

SA INSPECTION DEPARTMENT APPROVED CONTRACTOR AGENCY

Client Satisfaction and Service Feedback

Survey questions

		Answers	Remarks
1	Did the Service provider Co. provide the right inspector with a valid qualification card?	Yes	
2	Did the service provider Co. respond for inspection within the expected time frame?	Yes	
3	Was the inspector wearing the required personal protective equipment (PPE) during the inspection?	Yes	
4	Did the inspection conducted safely and in accordance with Aramco's standards?	Yes	

For any enquiry or concern, please contact: Inspection Dept. - ISSD Crane Inspection Unit (CIU)


SPECIFICATIONS

Size	Metric	British
Max. Working Height(Inside) A	14.30m	46ft 11in
Max. Working Height(Outside)	14.30m	46ft 11in
Max. Platform Height(Inside) B	12.30m	40ft 4in
Max. Platform Height(Outside)	12.30m	40ft 4in
Overall Length(Without Outriggers)	3.19m	10ft 6in
Overall Length(With Outriggers) C	3.84m	12ft 7in
Overall Width D	1.76m	5ft 9in
Overall Height(Rails Up) E	2.74m	9ft
Overall Height(Rails Down) F	1.97m	6ft 6in
Platform Size(Length×Width)	2.88m×1.52m	9ft 5in × 5ft
Platform Extension Size G	1.43m	4ft 8in
Ground Clearance	0.24m	9in
Wheelbase H	2.29m	7ft 6in
Turning Radius(Inside/Outside)	2.15m/4.85m	7ft 1in/15ft 11in
Tyres	26×12-16.5	26×12-16.5

Performance		
S.W.L	363kg	800lb
S.W.L On Extension	136kg	299lb
Max. Occupants(Inside/Outside)	3/2	3/2
Gradeability	40%	40%
Travel Speed(Stowed)	5.00km/h	3.10mph
Travel Speed(Raised)	0.45km/h	0.28mph
Max. Working Slope	X-1.5°/Y-3°	X-1.5°/Y-3°
Up/Down Speed	45/46sec	45/46sec

Weight		
Overall Weight	5050kg	11133lb

Power		
Diesel Engine	18.2kW/3000rpm	18.2kW/3000rpm
Diesel Tank	47L	12.4gal
Hydraulic Tank	71L	18.7gal

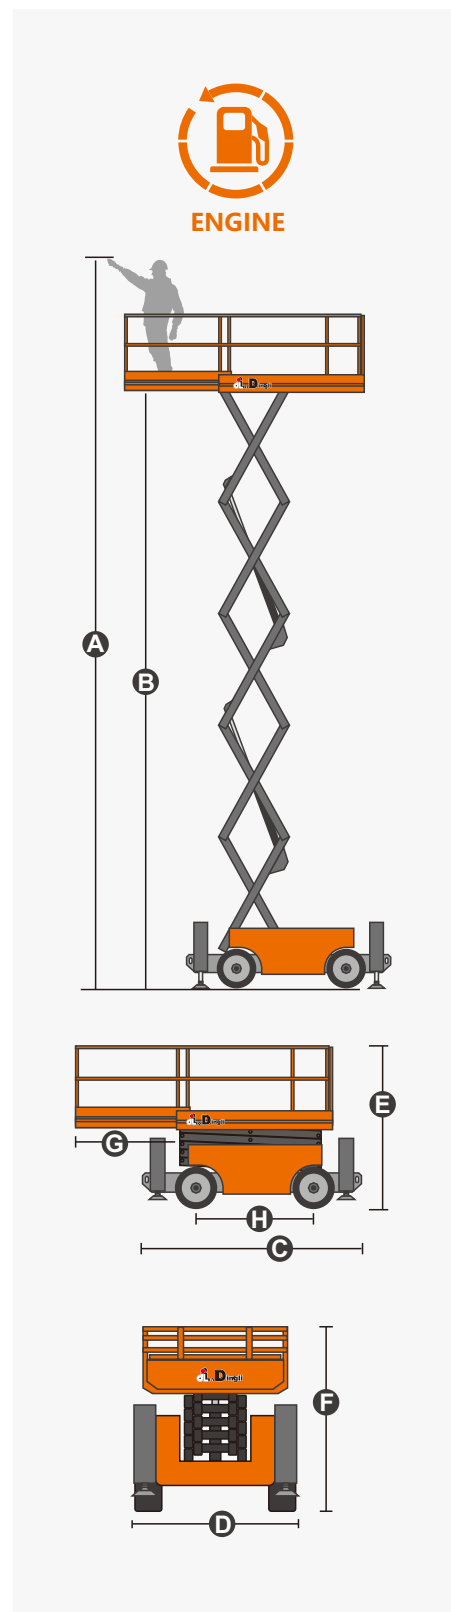

ANSI A92.20, CSA B354.6.17

FEATURES

Standard Items

- Proportional Joystick Controls
- Self-Locking Gates
- One-Way Platform Extension Deck
- Four-Wheel Drive
- Two-Wheel Steering
- Automatic Braking System
- Self-Weight Lowering System
- Tubing Explosion-Proof System
- Onboard Fault Diagnostic System
- Tilt Alarm
- Motion Alarm
- Horn
- Hour Meter
- Hydraulic Oil Cooling System
- Flashing LED Beacon
- Foldable Guard Rails
- Drive Enable
- Manual Brake Release
- Lanyard Attachment Point
- Standard Transport Forklift Pockets
- Tie-Down And Lifting Points
- Automatic Leveling Hydraulic Outriggers
- Anti-Restart Engine Protection
- Emergency Stop Button
- Platform Load Sense System
- Drivable At Full Height
- Oscillating Axle Chassis



ZHEJIANG DINGLI MACHINERY CO., LTD.

Address: No.188 Qihang Road, Deqing, Zhejiang P.R.C 313219

Telephone: +86(572)8681688

E-Mail: export@cndingli.com

<https://en.cndingli.com>

Due to continuous technology updates, technical parameters are subject to change without notice. This picture book is for reference only, the actual product shall prevail. The copyright is owned by zhejiang dingli, any content may not be copied for any purpose without written permission.

2022-09

