

OWNERSHIP CERTIFICATE

To Whom It May Concern

This is to certify that the following equipment listed below is the sole property of Sudhir Equipment Rental Company:

Equipment	Crane
Brand / Make	SANY
Asset ID	SRC-RT-060-003
Model Number	SRC600C
Serial Number	RC0060CA0041
Capacity	60 TON
Type	Rough Terrain Crane
Manufacturing Year	2020

This certification is issued to confirm the ownership status of the aforementioned equipment. Sudhir Equipment Rental Company holds full legal ownership rights over the listed equipment and retains all associated benefits and responsibilities. Should there be any queries or requests for verification regarding the ownership of the mentioned equipment, please do not hesitate to contact us at : Info@sudhirrentals.com

Sincerely,

Ajay Koul
General Manager
Sudhir Equipment Rental Company



KINGDOM OF SAUDI ARABIA
MINISTRY OF INTERIOR

رخصة سير
VEHICLES REGISTRATION

المملكة العربية السعودية
وزارة الداخلية

المالك شركة سودهير لتأجير المعدات شركة الشخص الواحد
المستخدم

هوية المالك ٧٠١٦١٥٨٣٣٤ هوية المستخدم

رقم الهيكل LFCNN35D8L2000049

رقم اللوحة ٥٤٤١ أ ب أ

5441 B A A

نوع التسجيل اشغال عامة

طراز المركبة كرين

حمولة المركبة ٣

سنة الصنع ٢٠٢٠

ماركة المركبة سباتي

وزن المركبة ٤٦٠٠ كجم

اللون أزرق

الرقم التسلسلي ٣٣٢٩٠٨١١





بروج للتأمين التعاوني
Buruj Cooperative Insurance

شهادة التأمين - CERTIFICATE OF INSURANCE

Policy Holder Name	:	Sudhir Equipment Rental Company	:	اسم حامل الوثيقة
Policy Number	:	01/CPM/ 2025/000002	:	رقم الوثيقة
Policy Period	:	05/04/ 2025 to 04/04/2026	:	فترة الوثيقة
Description of Machinery / Equipment	:	SANY-CRANE - 5441-BAA-SRC600C	:	وصف المعدة/ال لة
Chassis / Serial No.	:	945290810	:	رقم الهيكل/ التسلسلي
Year of Manufacturing	:	2020	:	سنة الصنع
Asset ID No.	:	SRC-RT-060-003	:	رقم ال صل
Location	:	Kingdom of Saudi Arabia.	:	الموقع

BURUJ Cooperative Insurance Company certifies that above client is holding a Machinery/Equipment Insurance Policy for the above-mentioned Equipment in accordance with the above-mentioned Insurance Policy.

With effect from: 05/04/ 2025 to 04/04/2026

This Certificate has been issued upon Insured's request as per all terms and conditions, exclusions, warranties mentioned in the policy.

تشهد شركة بروج للتأمين التعاوني بأن السادة أعل ه مؤمنين لديها تأمين المكان/المعدات المذكورة أعل ه وذلك حسب وثيقة التأمين المذكورة أعل ه

والتي يبدأ تاريخ سريانها من ٢٠٢٥/٠٤/٠٥ إلى ٢٠٢٦/٠٤/٠٤

تم إصدار هذه الشهادة بناءً على طلب المؤمن له وذلك حسب الشروط وال استثناءات وال شتراطات المذكورة في الوثيقة.

Important Notices:

1. This Certificate does not pay any fines, penalties, bonds or cautions that may be imposed.
2. Original certificates are only accepted.
3. Due to the importance of correct information being stated in this certificate, kindly examine the document carefully and advise the Company of any difference.
4. In the event of changes in the above information, kindly contact +966-11-2938383

مل حظات هامة:

- ١) ل تطبق هذه الشهادة التأمين على الغرامات والعقوبات المالية بما في ذلك المخالفات أو الضمانات أو الكفالات التي قد تقرر.
- ٢) تقبل الشهادة ال صلية فقط.
- ٣) نظراً ل همية صحة البيانات الخاصة بكم في هذه الشهادة، الرجاء التأكد منها وإشعار الشركة في حالة وجود أي اختل فات.
- ٤) عند الحاجة إلى تعديل البيانات أعل ه يرجى ال اتصال على شركة بروج للتأمين التعاوني ٢٩٣٨٣٨٣-١١-٩٦٦+



BURUJ Cooperative Insurance Company

P.O. Box 51855, Riyadh 11553,

National Address 3385, Al Thomamah Road, An-Nada District.

800 124 0201 | burujinsurance.com

Issue Date: 3 April 2025



CERTIFICATE OF TEST AND THOROUGH EXAMINATION OF MOBILE CRANE

Cert. No.: 1624472	Date of Examination: 19/03/2024	Sticker No.: Load test
---------------------------	--	-------------------------------

Name & address of owner of the equipment		SUDHIR EQUIPMENT RENTAL CO.
Inspection requested by		SUDHIR EQUIPMENT RENTAL CO.
Place of inspection		DMM YARD
Type of inspection		TEST & THOROUGH EXAMINATION
Relevant regulation / Standard		ASME B30.5
Date of previous inspection / load test		19/03/2024 Not applicable
Identification & Description of the Equipment	Manufacturer name	SANY
	Equipment Type	RT MOBILE CRANE
	Nature of power	DEISEL POWERED
	Model / Year	SRC600C
	Serial number	A0041
	Owner ID / Registration number	SRC-RT-060-003
	Rated Capacity (maximum)	60 t
	Present Configuration	Main hoist current capacity: 60 t with 6 falls Auxiliary hoist current capacity: 5.6 t with 1
	Radius (Mini / Max)	Minimum: 3 m; Maximum: 36 m
	Length of Boom	Minimum: 11.3 m; Maximum: 43.5 m
	Counterweight (mass)	Standard from Manufacturer
	Wire rope specification	21 mm
	Complementary devices	N/A

Description of test: Visual inspection was carried out, followed by full functional testing.	Length of boom (m)	Radius (m)	Reeving (No. of falls)	Test Load	Safe Working Load
	15.3 m	7 m	6 falls	27500 kg	27500 kg
	19.3 m	10 m	6 falls	16000 kg	16000 kg
	27.4 m	18 m	6 falls	5200 kg	5200 kg

Note: "This certificate does not cover the use of the equipment for Personnel/Man riding purposes".

Result of Examination:

The above mentioned equipment has been found satisfactory at the time of inspection and is considered to be safe for further use, subject to continuous maintenance being applied and qualified operator being employed.

This is to certify that the Competent Person did attend at the said premises on said date to witness proof load test and/or to carry out thorough examination of the equipment described herein and that all particulars described above were correct at the time of examination. This Certificate becomes void in case of any major repair, modification and /or alteration being un-authorized by issuer of hereof.

Next Proof Load Test Due: 18/03/2029 or After Major Repair/Modifications	Next Inspection Due is on or before: 18/03/2025
---	--

Issued at Al Khobar on 05/05/2025

Inspector to Bureau Veritas
Signature:



Name: Mohamed OMARA
Position: Senior Inspector



Reviewed by
Signature:



Name: Abdullah SHEHRI
Position: Operations Manager

The technical conclusions thus expressed may have to be reconsidered in light of any modifications or alterations that would invalidate the data shown in the present certificate. These conclusions would become null & void should Bureau Veritas not be kept informed of such modifications or alterations with specific reference to the present certificate.

Any person not a party to the contract pursuant to which this document is delivered may not assert a claim against Bureau Veritas for any liability arising out of errors or omissions which may be contained in said document, or for errors of judgement, fault or negligence committed by the personnel of the Society or of its Agents in the establishment or issuance of this document, and in connection with any activities for which it may provide.

This not is NOT an indication that the item(s) is (are) fit for any specific purpose and does not release the manufacture, supplier and any party from their respective duty, guarantee, obligation and/or indemnity relating to, without limitation patents, workmanship, materials, safety, performance in operation and/or reliability.



CHECKLIST OF TEST & THOROUGH EXAMINATION OF MOBILE CRANE

Cert. No.: 1624472	Date of Examination: 19/03/2024	
SECTION	CONDITION	REMARKS
1. ACCESS		
1.1 Access to the cabin/control station	Satisfactory	
1.2 Access for maintenance operation	Satisfactory	
2. CHASSIS		
2.1 Chassis	Satisfactory	
2.2 Traveling device (tire, crawler)	Satisfactory	
2.3 Outriggers	Satisfactory	
2.4 Outrigger sole (shoe or pad)	Satisfactory	
2.5 None return valve on outrigger	Satisfactory	
2.6 Locking of suspensions	Satisfactory	
2.7 Locking of outriggers rest position	Satisfactory	
3. STRUCTURE OF EQUIPMENT		
3.1 Structure, A frame	Satisfactory	
3.2 Jib, fly jib	Satisfactory	STOWED
3.3 Pendants	Not applicable	
3.4 Counter weight	Satisfactory	
4. MECHANISM		
4.1 Main Hoisting mechanism	Satisfactory	
4.2 Aux. Hoisting mechanism	Satisfactory	
4.3 Hydraulic system	Satisfactory	
4.4 Cylinders	Satisfactory	
4.5 Hoisting brake system	Satisfactory	
4.6 Limitation of the lowering speed	Satisfactory	
4.7 Telescoping mechanism	Satisfactory	
4.8 Luffing mechanism	Not applicable	
4.9 Pivoting joints	Satisfactory	
4.10 Brake of slewing motion	Satisfactory	



4.11 Traveling Brake	Satisfactory	
4.12 Guards for moving parts	Satisfactory	
4.13 Motor	Satisfactory	
4.14 Gear box	Satisfactory	
5. LIFTING SYSTEM		
5.1 Wire rope / chain	Satisfactory	
5.2 Wire/chain rope end termination	Satisfactory	
5.3 Drum, pulley, return pulley	Satisfactory	
5.4 Hooks & hook blocks	Satisfactory	
5.5 Other load handling devices	Satisfactory	
6. ENERGY		
6.1 Main switch locking	Satisfactory	
6.2 Equipment and cabling	Satisfactory	
6.3 Protection of live parts/enclosure	Satisfactory	
6.4 Lighting of the crane/site	Satisfactory	
7. CABIN / CONTROL STATION		
7.1 Structure	Satisfactory	
7.2 Visibility / windows	Satisfactory	
7.3 Heating / AC system	Satisfactory	
7.4 Seat	Satisfactory	
7.5 Fire extinguisher	Satisfactory	
7.6 Identification of the controls	Satisfactory	
7.7 Control dead man type	Satisfactory	
7.8 General stopping device by key	Satisfactory	
7.9 Emergency stop button	Satisfactory	
7.10 Level indicator	Satisfactory	
7.11 Angle Indicator	Satisfactory	
7.12 Horn	Satisfactory	
7.13 Traffic lights	Satisfactory	
7.14 Direction Indicators	Satisfactory	
8. SAFETY DEVICES		



BUREAU
VERITAS



8.1 Hoisting limiter/Anti Two Blocks	Satisfactory	
8.2 Luffing limiter	Not applicable	
8.3 Telescopic limiter	Satisfactory	
8.4 Slewing limiter	Satisfactory	
8.5 Load limiter	Satisfactory	
8.6 Level limiter	Satisfactory	
8.7 Rated capacity indicator (RCI) / ASLI	Satisfactory	
8.8 None return valve on piston	Satisfactory	
8.9 Other limiter or indicator	Satisfactory	
9. MISCELLANEOUS REQUIREMENTS		
9.1 Maker plate	Satisfactory	
9.2 Load chart	Satisfactory	
9.3 Wire rope certificate	Satisfactory	
9.4 General Safety Requirements	Satisfactory	
Notes : - Maintain proper housekeeping & preventive maintenance.		
Next Proof Load Test Due: 18/03/2029 or After Major Repair/Modifications		Next Inspection Due is on or before: 18/03/2025

Inspector to Bureau Veritas
Signature:



Name: Mohamed OMARA
Position: Senior Inspector

Vehicle Details

Submit the Vehicle Update Request

Owner Id Number7016158334

License issue date1442-04-07

Branch Id

Actual Driver Id Number

Plate registration typeEquipment

Sequence Number33290810

Vehicle Modelرافعه شوکیه

Vehicle Load2

Model Year2020

Chassis NumberLFCNN35D8L2000049

MVPI StatusEXPIRED

Insurance StatusValid

Actual Driver Start Date

Ownership Start Date

license Expiry Date1448-04-07

Branch name

Actual Driver Name

Plate Info

٥٤٤١	ا ا ب
5441	B A A

Vehicle Makerههههه

Vehicle Colorازرق

Vehicle Weight42000

Restriction StatusNot Restricted

Vehicle Statusvalid

MVPI Expiry Hijri Date1446-09-17

Insurance Expiry Date2025-11-14

No. LFT-S.
01 - 74095




BUREAU
VERITAS

Saudi Arabia

Tel: +966 13 882 1071

Fax: +966 13 882 1072



[Mobile Crane]
EQUIP. NO. SRC-RT-060-003

EQUIP. S N. RC0060CA0041

S. W. L: 60 Ton

DATE OF INSPECTION 22-may-2025

NEXT INSPECTION DUE ON 21-may-2026

INSPECTED BY Mohamed Zouhry

This sticker is issued under Bureau veritas General
Conditions of Service and is valid only in conjunction
with hereafter inspection Report No.
Report No. LFT-R



CERTIFICATE OF TEST AND THOROUGH EXAMINATION OF MOBILE CRANE

Cert. No.: 1940937	Date of Examination: 22/05/2025	Sticker No.: 01-74095
---------------------------	--	------------------------------

Name & address of owner of the equipment		Sudhir Equipment Rental Company			
Inspection requested by		Sudhir Equipment Rental Company			
Place of inspection		Dammam Yard.			
Type of inspection		TEST & THOROUGH EXAMINATION			
Relevant regulation / Standard		ASME B30.5			
Date of previous inspection / load test					
Identification & Description of the Equipment	Manufacturer name	Sany			
	Equipment Type	Mobile Crane			
	Nature of power	DEISEL POWERED			
	Model / Year	SRC600C/ 2020			
	Serial number	RC0060CA0041			
	Owner ID / Registration number	SRC-RT-060-003			
	Rated Capacity (maximum)	60 Ton			
	Present Configuration	Main hoist current capacity: 60 Ton with 6 Part Of Line Auxiliary hoist current capacity: 6 Ton with 1 Line			
	Radius (Mini / Max)	Minimum: 3 Mtr; Maximum: 36 Mtr			
	Length of Boom	Minimum: 11.3 Mtr; Maximum: 43.5 Mtr			
	Counterweight (mass)	Standard from Manufacturer			
	Wire rope specification	20 mm			
	Complementary devices	-			

Description of test: Visual & Function Test inspection was carried out, followed by full functional testing.	Length of boom (m)	Radius (m)	Reeving (No. of falls)	Test Load	Safe Working Load
	-	-	-	-	-
	-	-	-	-	-
	-	-	-	-	-

Note: "This certificate does not cover the use of the equipment for Personnel/Man riding purposes".

Result of Examination: The above mentioned equipment has been found satisfactory at the time of inspection and is considered to be safe for further use, subject to continuous maintenance being applied and qualified operator being employed. This is to certify that the Competent Person did attend at the said premises on said date to witness proof load test and/or to carry out thorough examination of the equipment described herein and that all particulars described above were correct at the time of examination. This Certificate becomes void in case of any major repair, modification and /or alteration being un-authorized by issuer of hereof.

Next Proof Load Test Due: or After Major Repair/Modifications	Next Inspection Due is on or before: 21/05/2026
--	--

Issued at Al Khobar on 25/05/2025

Inspector to Bureau Veritas
Signature:



Name: Mohamed Elsabry
Position: Inspector



Reviewed by
Signature:



Name: Abdullah SHEHRI
Position: Operations Manager

The technical conclusions thus expressed may have to be reconsidered in light of any modifications or alterations that would invalidate the data shown in the present certificate. These conclusions would become null & void should Bureau Veritas not be kept informed of such modifications or alterations with specific reference to the present certificate. Any person not a party to the contract pursuant to which this document is delivered may not assert a claim against Bureau Veritas for any liability arising out of errors or omissions which may be contained in said document, or for errors of judgement, fault or negligence committed by the personnel of the Society or of its Agents in the establishment or issuance of this document, and in connection with any activities for which it may provide. This not is NOT an indication that the item(s) is (are) fit for any specific purpose and does not release the manufacture, supplier and any party from their respective duty, guarantee, obligation and/or indemnity relating to, without limitation patents, workmanship, materials, safety, performance in operation and/or reliability.
--



CHECKLIST OF TEST & THOROUGH EXAMINATION OF MOBILE CRANE

Cert. No.: 1940937	Date of Examination: 22/05/2025
---------------------------	--

SECTION	CONDITION	REMARKS
1. ACCESS		
1.1 Access to the cabin/control station	Satisfactory	
1.2 Access for maintenance operation	Satisfactory	
2. CHASSIS		
2.1 Chassis	Satisfactory	
2.2 Traveling device (tire, crawler)	Satisfactory	
2.3 Outriggers	Satisfactory	
2.4 Outrigger sole (shoe or pad)	Satisfactory	
2.5 None return valve on outrigger	Satisfactory	
2.6 Locking of suspensions	Satisfactory	
2.7 Locking of outriggers rest position	Satisfactory	
3. STRUCTURE OF EQUIPMENT		
3.1 Structure, A frame	Satisfactory	
3.2 Jib, fly jib	Satisfactory	
3.3 Pendants	Satisfactory	
3.4 Counter weight	Satisfactory	
4. MECHANISM		
4.1 Main Hoisting mechanism	Satisfactory	
4.2 Aux. Hoisting mechanism	Satisfactory	
4.3 Hydraulic system	Satisfactory	
4.4 Cylinders	Satisfactory	
4.5 Hoisting brake system	Satisfactory	
4.6 Limitation of the lowering speed	Satisfactory	
4.7 Telescoping mechanism	Satisfactory	
4.8 Luffing mechanism	Not applicable	
4.9 Pivoting joints	Satisfactory	
4.10 Brake of slewing motion	Satisfactory	



4.11 Traveling Brake	Satisfactory	
4.12 Guards for moving parts	Satisfactory	
4.13 Motor	Satisfactory	
4.14 Gear box	Satisfactory	
5. LIFTING SYSTEM		
5.1 Wire rope / chain	Satisfactory	
5.2 Wire/chain rope end termination	Satisfactory	
5.3 Drum, pulley, return pulley	Satisfactory	
5.4 Hooks & hook blocks	Satisfactory	
5.5 Other load handling devices	Satisfactory	
6. ENERGY		
6.1 Main switch locking	Satisfactory	
6.2 Equipment and cabling	Satisfactory	
6.3 Protection of live parts/enclosure	Satisfactory	
6.4 Lighting of the crane/site	Satisfactory	
7. CABIN / CONTROL STATION		
7.1 Structure	Satisfactory	
7.2 Visibility / windows	Satisfactory	
7.3 Heating / AC system	Satisfactory	
7.4 Seat	Satisfactory	
7.5 Fire extinguisher	Satisfactory	
7.6 Identification of the controls	Satisfactory	
7.7 Control dead man type	Satisfactory	
7.8 General stopping device by key	Satisfactory	
7.9 Emergency stop button	Satisfactory	
7.10 Level indicator	Satisfactory	
7.11 Angle Indicator	Satisfactory	
7.12 Horn	Satisfactory	
7.13 Traffic lights	Satisfactory	
7.14 Direction Indicators	Satisfactory	
8. SAFETY DEVICES		



BUREAU
VERITAS



8.1 Hoisting limiter/Anti Two Blocks	Satisfactory	
8.2 Luffing limiter	Not applicable	
8.3 Telescopic limiter	Satisfactory	
8.4 Slewing limiter	Satisfactory	
8.5 Load limiter	Satisfactory	
8.6 Level limiter	Satisfactory	
8.7 Rated capacity indicator (RCI) / ASLI	Satisfactory	
8.8 None return valve on piston	Satisfactory	
8.9 Other limiter or indicator	Satisfactory	
9. MISCELLANEOUS REQUIREMENTS		
9.1 Maker plate	Satisfactory	
9.2 Load chart	Satisfactory	
9.3 Wire rope certificate	Satisfactory	
9.4 General Safety Requirements	Satisfactory	
Notes :		
Next Proof Load Test Due: or After Major Repair/Modifications		Next Inspection Due is on or before: 21/05/2026


Inspector to Bureau Veritas
Signature:

Mohamed Elsabry




Name: Mohamed Elsabry
Position: Inspector

Boom Operating Range

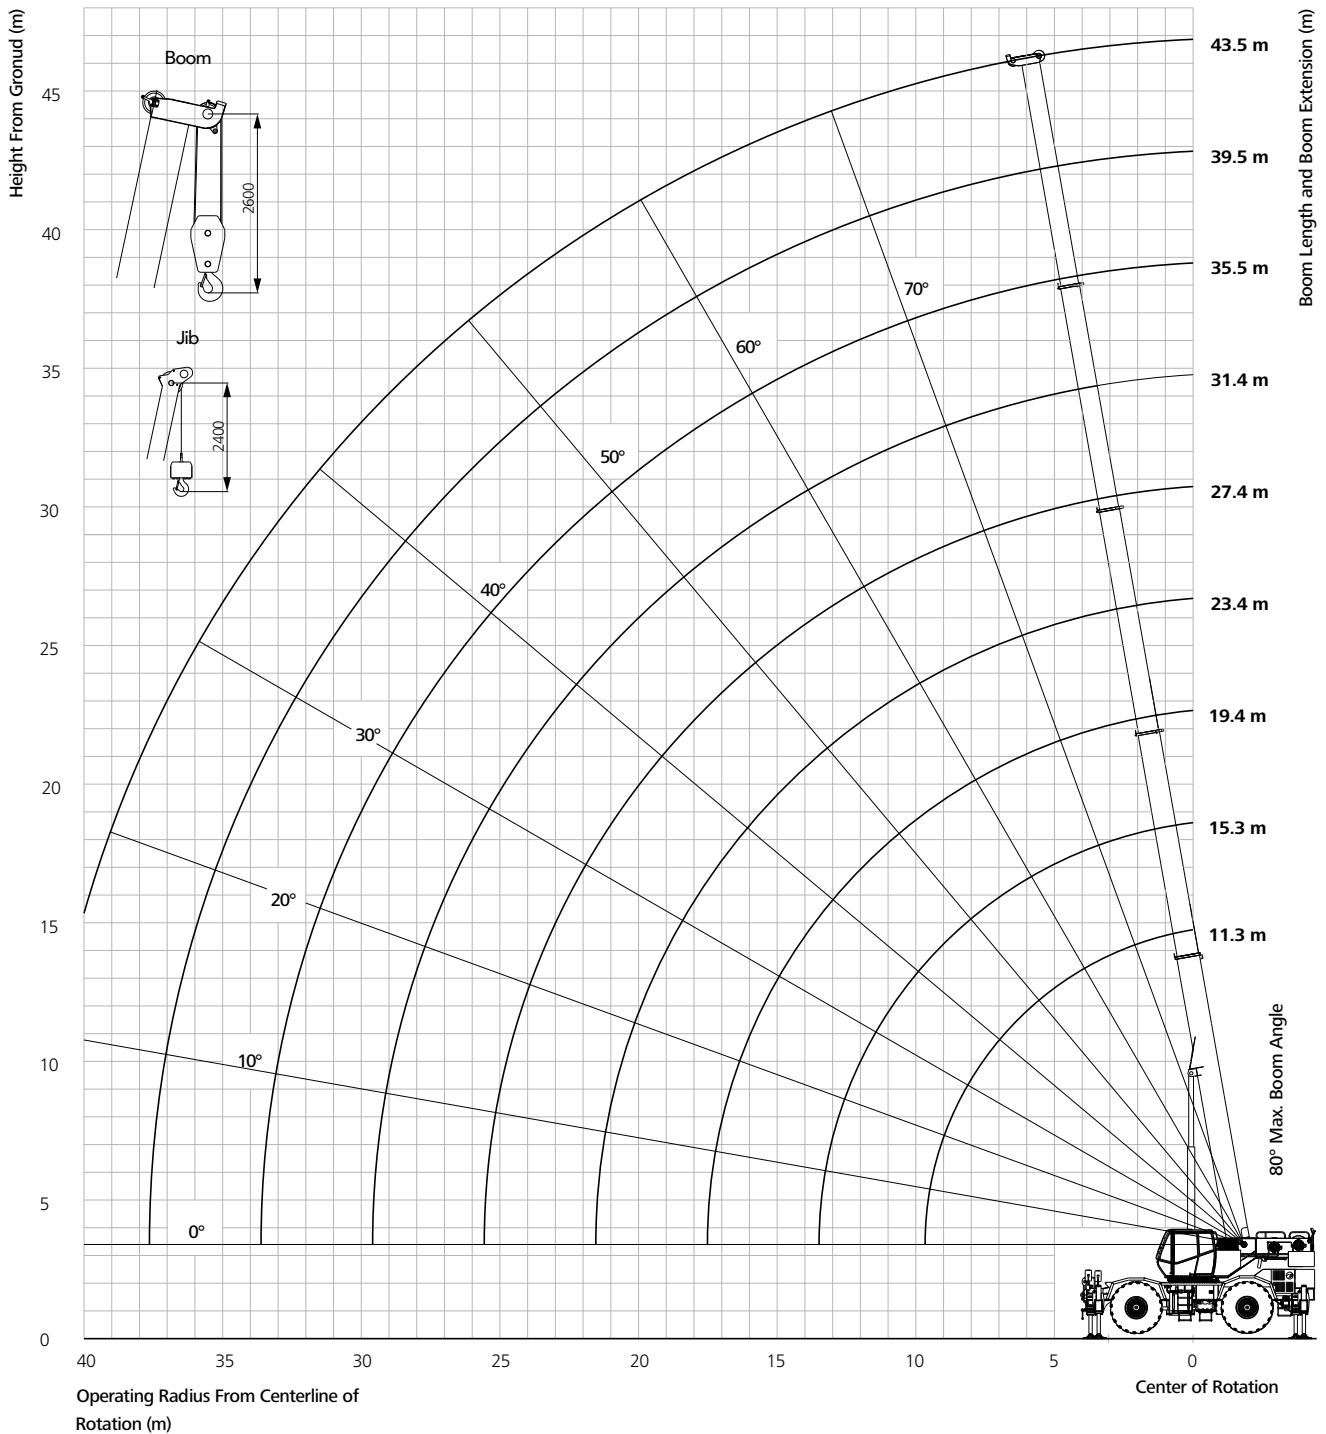

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35		23.38		27.40		31.43		35.45		39.48		43.50	Radius (m)
3.0	60.00	45.00	35.00	22.00												3.0
3.5	57.00	45.00	35.00	22.00	25.00	20.00										3.5
4.0	54.00	45.00	35.00	22.00	25.00	20.00	22.50	17.05								4.0
4.5	47.80	43.00	33.00	22.00	25.00	20.00	22.50	17.05	17.50	15.00						4.5
5.0	43.00	41.00	32.00	22.00	24.50	20.00	22.00	17.05	17.50	15.00						5.0
5.5	39.00	38.00	32.00	22.00	24.20	20.00	21.50	17.05	17.50	15.00	15.50	11.00				5.5
6.0	35.50	34.70	32.00	22.00	23.80	19.50	20.50	17.05	17.50	14.50	14.50	11.00				6.0
6.5	32.50	32.00	30.50	22.00	22.30	19.00	19.80	16.30	17.50	14.00	14.00	11.00	12.50	10.00		6.5
7.0	30.00	29.70	29.00	22.00	21.50	18.50	18.80	15.70	17.50	13.50	14.00	11.00	12.00	10.00	9.50	7.0
7.5	27.80	27.50	26.00	22.00	21.00	18.00	18.00	15.00	17.50	13.00	13.00	11.00	11.50	10.00	9.50	7.5
8.0	25.80	25.00	23.50	22.00	20.00	17.50	17.20	14.50	16.50	12.50	12.50	11.00	11.00	10.00	9.50	8.0
9.0	20.00	20.00	19.50	21.70	18.00	17.00	16.50	13.50	15.00	12.00	12.00	10.30	10.50	10.00	9.30	9.0
10.0		16.00	16.00	17.80	16.00	12.50	15.00	12.50	13.50	11.00	11.50	9.60	10.00	9.60	9.00	10.0
12.0		10.90	11.00	12.80	12.00	12.00	11.80	10.70	11.00	10.00	10.00	8.60	9.00	9.10	8.30	12.0
14.0			7.70	9.80	8.50	9.50	8.80	9.35	8.60	8.60	8.50	7.80	8.00	8.60	8.00	14.0
16.0			5.50	7.50	6.00	7.80	6.80	8.05	6.90	7.20	7.10	6.75	7.30	7.60	7.35	16.0
18.0					4.50	6.50	5.20	6.55	5.60	6.20	5.70	6.05	6.00	6.20	5.80	18.0
20.0					3.40	5.30	4.10	5.35	4.40	5.20	4.50	5.25	4.80	4.90	4.70	20.0
22.0							3.15	4.45	3.30	4.40	3.55	4.55	3.70	4.15	3.80	22.0
24.0							2.45	3.65	2.50	3.60	2.85	3.75	2.90	3.35	3.10	24.0
26.0									1.90	3.10	2.25	3.25	2.30	2.85	2.50	26.0
28.0									1.50	2.60	1.75	2.75	1.90	2.35	2.00	28.0
30.0											1.35	2.35	1.50	1.95	1.60	30.0
32.0											1.00	1.95	1.20	1.55	1.25	32.0
34.0													0.90	1.25	0.95	34.0
36.0													0.70	1.05		36.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	0%	100%	0%	100%	50%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	5st boom
Number of parts of line	10	10	8	8	6	6	4	4	4	4	4	4	4	4	3	Number of parts of line

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	31.43	35.45	39.48	43.50	Radius (m)
3.0	55.00	45.00	35.00	22.00						3.0
3.5	50.00	41.00	32.50	21.00	25.00	20.00				3.5
4.0	44.40	37.00	30.50	19.80	24.00	19.00	22.50	18.50		4.0
4.5	38.00	33.50	29.00	18.80	22.50	18.00	21.50	17.20	17.50	4.5
5.0	32.00	30.00	26.50	17.50	21.50	16.50	20.80	15.00	17.20	5.0
5.5	27.00	25.50	23.50	16.20	20.80	15.00	20.40	13.80	17.00	5.5
6.0	22.50	21.50	20.00	15.00	20.00	14.20	19.80	13.20	16.50	6.0
6.5	19.00	18.00	17.50	14.20	18.00	13.50	18.00	12.80	15.80	6.5
7.0	16.00	15.50	15.20	13.50	15.40	13.00	15.50	12.40	14.80	7.0
7.5	14.00	13.80	13.00	13.00	13.50	12.50	13.80	12.00	13.50	7.5
8.0	12.00	12.00	11.00	12.40	12.20	12.00	12.50	11.50	12.20	8.0
9.0	9.50	9.50	9.60	11.20	9.80	11.00	10.00	10.60	10.00	9.0
10.0		7.40	7.60	9.70	7.80	9.50	8.00	9.20	8.30	10.0
12.0		5.00	5.00	7.20	5.30	7.00	5.40	6.80	5.50	12.0
14.0			3.40	5.40	3.70	5.30	3.90	5.20	4.00	14.0
16.0			2.20	3.80	2.60	3.70	2.80	3.70	2.90	16.0
18.0					1.80	2.70	2.00	2.80	2.10	18.0
20.0					1.20	2.10	1.50	2.20	1.60	20.0
22.0							0.90	1.70	1.10	22.0
24.0								1.30		24.0
26.0									1.00	26.0
28.0									0.90	28.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	5st boom
Min boom angle	20	25	25	20	20	20	30	20	40	Min boom angle
Number of parts of line	10	10	8	8	6	6	4	4	4	Number of parts of line


Load Chart - Telescopic Boom

Unit: t




Radius (m)	11.30	15.33	19.35		23.38		27.40		31.43		35.45		39.48		43.50	Radius (m)
3.0	30.00	30.00	25.00	22.00												3.0
3.5	24.80	24.00	23.50	20.50	20.00	20.00										3.5
4.0	18.80	18.00	17.50	18.00	17.00	17.80	16.50	17.50								4.0
4.5	15.20	14.50	13.50	15.50	14.00	15.50	14.00	15.20	14.00	15.00						4.5
5.0	12.90	12.00	11.40	13.50	11.80	13.50	12.00	13.20	12.00	13.00						5.0
5.5	11.20	10.50	10.00	11.50	10.20	11.50	10.50	11.50	10.80	11.20	10.50	11.00				5.5
6.0	9.80	9.00	8.50	10.20	9.00	10.20	9.20	10.20	9.50	10.00	9.20	9.80	9.00	9.20		6.0
6.5	8.60	8.00	7.50	8.80	7.80	8.90	8.00	9.00	8.20	9.00	8.20	9.00	8.20	8.40		6.5
7.0	7.60	7.00	6.50	7.80	7.00	7.90	7.20	8.00	7.30	8.00	7.30	8.00	7.40	7.60	7.40	7.0
7.5	6.60	6.00	5.60	7.00	6.20	7.10	6.50	7.20	6.50	7.20	6.50	7.20	6.50	6.70	6.50	7.5
8.0	5.70	5.20	5.00	6.00	5.20	6.10	5.50	6.20	5.60	6.20	5.60	6.20	5.60	5.80	5.70	8.0
9.0	4.30	4.00	3.80	4.70	4.20	4.90	4.50	5.00	4.50	5.00	4.50	5.00	4.50	4.70	4.40	9.0
10.0		3.00	2.80	3.60	3.00	3.80	3.20	3.90	3.20	4.00	3.20	4.00	3.30	3.50	3.40	10.0
12.0		1.60	1.40	2.40	1.80	2.60	2.00	2.70	2.10	2.80	2.20	2.80	2.30	2.50	2.40	12.0
14.0				1.60	1.00	1.80	1.20	1.90	1.30	2.00	1.40	2.00	1.60	1.80	1.70	14.0
16.0				1.00		1.20		1.30	0.80	1.30	0.90	1.40	1.10	1.30	1.20	16.0
18.0								0.90		0.90		1.00	0.70	0.90	0.80	18.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	0%	100%	0%	100%	50%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	5st boom
Min boom angle	20	25	45	25	45	40	55	45	55	50	60	55	62	60	62	Min boom angle
Number of parts of line	10	8	6	6	6	6	4	4	4	4	4	4	4	4	4	Number of parts of line

Jib Operating Range

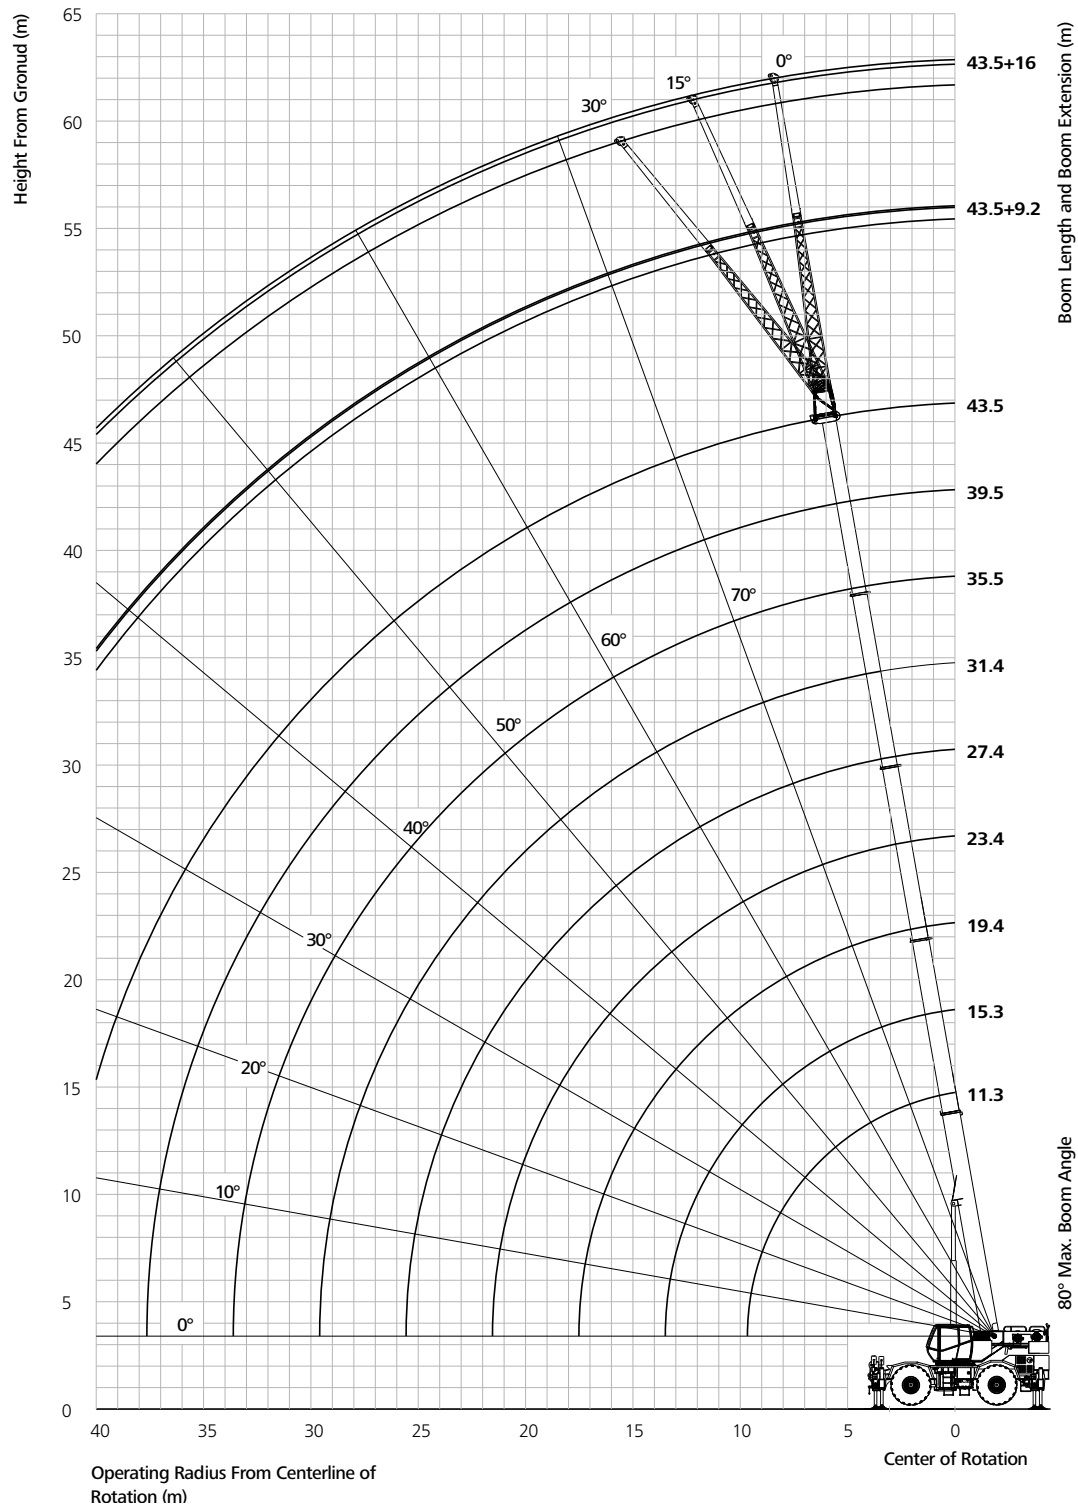

Load Chart - Fixed Jib

Unit: t



Working length of the boom	43.5m+9.2m			43.5m+16m			Working length of the boom
	0°	15°	30°	0°	15°	30°	
80	4.50	2.70	2.40	2.60	1.50	1.10	80
78	4.50	2.70	2.40	2.60	1.50	1.10	78
76	4.00	2.50	2.30	2.40	1.40	1.10	76
74	3.75	2.40	2.25	2.20	1.30	1.10	74
72	3.50	2.30	2.15	2.00	1.20	1.00	72
70	3.00	2.20	2.05	1.80	1.15	1.00	70
68	2.70	2.10	1.95	1.60	1.10	0.95	68
66	2.50	2.00	1.85	1.50	1.05	0.90	66
64	2.20	1.80	1.75	1.45	1.00	0.85	64
62	2.00	1.65	1.50	1.30	0.95	0.80	62
60	1.70	1.45	1.20	1.10	0.85	0.75	60
58	1.20	1.00	0.85	0.90	0.75	0.65	58
56	1.00	0.85	0.75	0.80	0.65	0.60	56
54	0.80	0.70	0.60	0.70	0.60		54
52	0.70	0.60	0.55				52
50	0.60						50
Min Angle(°)	48°	50°	50°	52°	52°	54°	Min Angle(°)

Load Chart - Telescopic Boom

Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	18.10	14.10	9.00			3
3.5	16.00	14.10	8.00	6.50		3.5
4	14.30	14.10	7.00	6.50		4
4.5	12.85	12.65	7.20	6.50	5.50	4.5
5	11.60	11.40	6.50	6.50	5.00	5
5.5	10.50	10.30	6.00	6.00	4.50	5.5
6	9.20	9.35	5.30	5.00	4.20	6
6.5	8.00	8.40	4.80	4.30	3.80	6.5
7	7.00	7.50	4.20	4.00	3.50	7
7.5	6.00	6.60	3.80	3.50	3.20	7.5
8	5.30	5.80	3.20	3.00	2.90	8
8.5	4.65	5.40	2.95	2.70	2.50	8.5
9	4.00	5.00	2.70	2.40	2.20	9
10		4.00	2.20	2.00	1.90	10
11			1.70	1.60	1.50	11
12				1.50	1.30	12
14					1.00	14
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines

Load Chart - Telescopic Boom

Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	20.00	16.00	15.00			3
3.5	20.00	16.00	15.00	11.00		3.5
4	20.00	16.00	14.00	11.00	10.00	4
4.5	17.50	15.00	13.00	11.00	10.00	4.5
5	14.50	13.00	12.00	11.00	10.00	5
5.5	12.00	11.00	11.00	10.00	10.00	5.5
6	10.30	10.00	10.00	9.50	9.50	6
6.5	9.10	9.00	8.80	9.00	9.20	6.5
7	7.80	7.90	8.00	8.00	8.00	7
7.5	6.80	6.90	7.00	7.20	7.50	7.5
8	6.00	6.00	6.00	6.50	7.10	8
8.5	5.20	5.00	5.00	6.00	6.30	8.5
9	4.50	4.50	4.00	5.00	5.50	9
10		3.50	3.00	4.00	4.20	10
11			2.00	3.30	3.80	11
12			1.00	2.80	3.00	12
14				1.80	2.00	14
16				1.00		16
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines

Load Chart - Telescopic Boom

Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	12.00	10.50	10.0			3
3.5	12.00	10.50	10.0			3.5
4	10.00	10.00	9.0	8.00		4
4.5	8.60	8.00	8.0	6.50	5.50	4.5
5	7.00	6.50	6.0	5.70	5.50	5
5.5	5.80	4.80	4.5	5.00	5.50	5.5
6	4.30	3.00	3.0	4.00	5.50	6
6.5	3.00	2.50	2.5	3.00	3.50	6.5
7	2.50	2.00	2.0	2.50	3.00	7
7.5	2.00	1.50	1.5	1.70	2.00	7.5
8	1.50	1.50	1.5	1.70	2.00	8
8.5		1.00	1.0	1.20	1.50	8.5
9					1.00	9
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines
