

SRC-RT-060-003



**BUREAU
VERITAS**



CERTIFICATE OF TEST AND THOROUGH EXAMINATION OF MOBILE CRANE

Cert. No.: 1624472	Date of Examination: 19/03/2024	Sticker No.: Load test
--------------------	---------------------------------	------------------------

Name & address of owner of the equipment		SUDHIR EQUIPMENT RENTAL CO.
Inspection requested by		SUDHIR EQUIPMENT RENTAL CO.
Place of inspection		DMM YARD
Type of inspection		TEST & THOROUGH EXAMINATION
Relevant regulation / Standard		ASME B30.5
Date of previous inspection / load test		19/03/2024Not applicable
Identification & Description of the Equipment	Manufacturer name	SANY
	Equipment Type	RT MOBILE CRANE
	Nature of power	DEISEL POWERED
	Model / Year	SRC600C
	Serial number	A0041
	Owner ID / Registration number	SRC-RT-060-003
	Rated Capacity (maximum)	60 t
	Present Configuration	Main hoist current capacity: 60 t with 6 falls
		Auxiliary hoist current capacity: 5.6 t with 1
	Radius (Mini / Max)	Minimum: 3 m; Maximum: 36 m
	Length of Boom	Minimum: 11.3 m; Maximum:43.5 m
	Counterweight (mass)	Standard from Manufacturer
	Wire rope specification	21 mm
Complementary devices	N/A	

Description of test: Visual inspection was carried out, followed by full functional testing.	Length of boom (m)	Radius (m)	Reeving (No. of falls)	Test Load	Safe Working Load
	15.3 m	7 m	6 falls	27500 kg	27500 kg
	19.3 m	10 m	6 falls	16000 kg	16000 kg
	27.4 m	18 m	6 falls	5200 kg	5200 kg

Note: "This certificate does not cover the use of the equipment for Personnel/Man riding purposes".

Result of Examination:

The above mentioned equipment has been found satisfactory at the time of inspection and is considered to be safe for further use, subject to continuous maintenance being applied and qualified operator being employed.

This is to certify that the Competent Person did attend at the said premises on said date to witness proof load test and/or to carry out thorough examination of the equipment described herein and that all particulars described above were correct at the time of examination. This Certificate becomes void in case of any major repair, modification and / or alteration being un-authorized by issuer of hereof.

Next Proof Load Test Due: or After Major Repair/Modifications	Next Inspection Due is on or before: 18/03/2025
---	---

Issued at Al Khobar on 31/03/2024

Inspector to Bureau Veritas
Signature:

Name: Mohamed OMARA
Position: Senior Inspector



Reviewed by
Signature:

Name: Abdullah SHEHRI
Position: Operations Manager

The technical conclusions thus expressed may have to be reconsidered in light of any modifications or alterations that would invalidate the data shown in the present certificate. These conclusions would become null & void should Bureau Veritas not be kept informed of such modifications or alterations with specific reference to the present certificate.

Any person not a party to the contract pursuant to which this document is delivered may not assert a claim against Bureau Veritas for any liability arising out of errors or omissions which may be contained in said document, or for errors of judgement, fault or negligence committed by the personnel of the Society or of its Agents in the establishment or issuance of this document, and in connection with any activities for which it may provide.

This is NOT an indication that the item(s) is (are) fit for any specific purpose and does not release the manufacturer, supplier and any party from their respective duty, guarantee, obligation and/or indemnity relating to, without limitation patents, workmanship, materials, safety, performance in operation and/or reliability.





**BUREAU
VERITAS**



4.11 Traveling Brake	Satisfactory	
4.12 Guards for moving parts	Satisfactory	
4.13 Motor	Satisfactory	
4.14 Gear box	Satisfactory	
5. LIFTING SYSTEM		
5.1 Wire rope / chain	Satisfactory	
5.2 Wire/chain rope end termination	Satisfactory	
5.3 Drum, pulley, return pulley	Satisfactory	
5.4 Hooks & hook blocks	Satisfactory	
5.5 Other load handling devices	Satisfactory	
6. ENERGY		
6.1 Main switch locking	Satisfactory	
6.2 Equipment and cabling	Satisfactory	
6.3 Protection of live parts/enclosure	Satisfactory	
6.4 Lighting of the crane/site	Satisfactory	
7. CABIN / CONTROL STATION		
7.1 Structure	Satisfactory	
7.2 Visibility / windows	Satisfactory	
7.3 Heating / AC system	Satisfactory	
7.4 Seat	Satisfactory	
7.5 Fire extinguisher	Satisfactory	
7.6 Identification of the controls	Satisfactory	
7.7 Control dead man type	Satisfactory	
7.8 General stopping device by key	Satisfactory	
7.9 Emergency stop button	Satisfactory	
7.10 Level indicator	Satisfactory	
7.11 Angle Indicator	Satisfactory	
7.12 Horn	Satisfactory	
7.13 Traffic lights	Satisfactory	
7.14 Direction Indicators	Satisfactory	
8. SAFETY DEVICES		



BUREAU
VERITAS



8.1 Hoisting limiter/Anti Two Blocks	Satisfactory	
8.2 Luffing limiter	Not applicable	
8.3 Telescopic limiter	Satisfactory	
8.4 Slewing limiter	Satisfactory	
8.5 Load limiter	Satisfactory	
8.6 Level limiter	Satisfactory	
8.7 Rated capacity indicator (RCI) / ASLI	Satisfactory	
8.8 None return valve on piston	Satisfactory	
8.9 Other limiter or indicator	Satisfactory	
9. MISCELLANEOUS REQUIREMENTS		
9.1 Maker plate	Satisfactory	
9.2 Load chart	Satisfactory	
9.3 Wire rope certificate	Satisfactory	
9.4 General Safety Requirements	Satisfactory	
Notes : - Maintain proper housekeeping & preventive maintenance.		
Next Proof Load Test Due: or After Major Repair/Modifications		Next Inspection Due is on or before: 18/03/2025

Inspector to Bureau Veritas
Signature:

Mohamed OMARA



Name: Mohamed OMARA
Position: Senior Inspector



1713356944363

الرقم المرجعي :

2024-04-17

تاريخ إصدار القائمة :

7016158334

رقم العميل:

شركة سودهير لتأجير المعدات

اسم العميل:

العدد الحقيقي لمجموع المركبات 63

اسم المستخدم الفعلي	هوية المستخدم الفعلي	حالة التأمين	تاريخ انتهاء رخصة السير	تاريخ الملكية	اللون الأساسي	رقم الهيكل	الرقم التسلسلي	سنة الصنع	الطراز	الماركة	الوضع	نوع الهيكل	نوع التسجيل	رقم اللوحة
MAJID MEWA QASIM	2064588540	ساري	1448-04-08	1442-04-08	الزرق	LFENN35DXL2000151	78490810	2020	كرين	سائي	صالحة		معدات ثقيلة	أ ب 5421
		ساري	1447-03-16	1438-03-16	رصاصي	JN18T2MU8GW005059	724237510	2016	أكس تريل	نيسان	صالحة		خاص	د أ هـ 5054
		ساري	1447-05-11	1444-05-11	أبيض	MR0DB8CD2H0115608	264305910	2017	يخب عمارتين	تويوتا	صالحة		نقل خاص	ب ص ك 4781
		ساري	1447-12-02	1444-12-02	فضي	MZBG8B8144PN082328	220949910	2023	كارنس واجن	كيا	صالحة		خاص	ر ص ق 5306
		ساري	1448-01-13	1445-01-13	أبيض	RKLB20DE8R4001253	71630020	2024	كوروبلا	تويوتا	صالحة		خاص	ر ص م 6431
		ساري	1448-04-07	1442-04-07	الزرق	LFENN35D2L2000032	395290810	2020	كرين	سائي	صالحة		معدات ثقيلة	أ ب 5418
		ساري	1445-12-22	1442-12-22	برتقالي	FDB08-1130-01647	593355810	2019	رافعة	دوسان	صالحة		معدات ثقيلة	أ ق 6012
		ساري	1447-03-16	1444-03-16	أبيض	JE3AB36U9HU712807	599093910	2017	لانسر	ميتسوبيشي	صالحة		خاص	ر د ص 2131
		ساري	1448-04-07	1442-04-07	الزرق	LFENN35D8L2000049	33290810	2020	رافعة شوكيه	معدده	صالحة		معدات ثقيلة	أ ب 5441
		ساري	1445-04-04	1442-04-04	الزرق	LFENN35DXL2000036	224090810	2020	كرين	سائي	صالحة		معدات ثقيلة	أ ب 5427
		ساري	1447-12-04	1444-12-04	أبيض	MPAER33T7PT006557	96069910	2023	يخب عمارتين	ايسوزو	صالحة		نقل خاص	ب ط ب 2930
		ساري	1446-10-22	1443-10-22	برتقالي	011002P8148	427901910	2022	رافعة شوكيه	هيلي	صالحة		معدات ثقيلة	أ ر 2218
		ساري	1447-02-23	1444-02-23	أبيض	KMH0741F6HU254660	207143910	2017	التترا	هونداي	صالحة		خاص	ر د ج 4464
MUSTAFA ABDUL	2520037231	ساري	1447-05-04	1444-05-04	أسود	MMBNGV549NH014296	866684910	2022	يخب عمارتين	ميتسوبيشي	صالحة		نقل خاص	ب ص ك 5946
		ساري	1447-07-21	1444-07-21	برتقالي	010702T6063	384256910	2023	رافعة شوكيه	هيلي	صالحة		معدات ثقيلة	أ ق 9413
		ساري	1446-08-16	1440-08-16	أبيض	JTEBU9FJ3KK166601	315611710	2019	برادو	تويوتا	صالحة		خاص	د ط ن 2153

NO.BV-23-1724



**BUREAU
VERITAS**
Tel.: 013 822 1071
Fax: 013 822 1072



EQUIP NO.: SRC-RT-060-003

EQUIP S. N. : A0041


DATE INSPECTED : 15/04/2024

NEXT INSPECTION DATE : 14/07/2024

INSPECTED BY : Mohamed OMARA


**SA INSPECTION DEPARTMENT APPROVED CONTRACTOR
AGENCIES**

Boom Operating Range

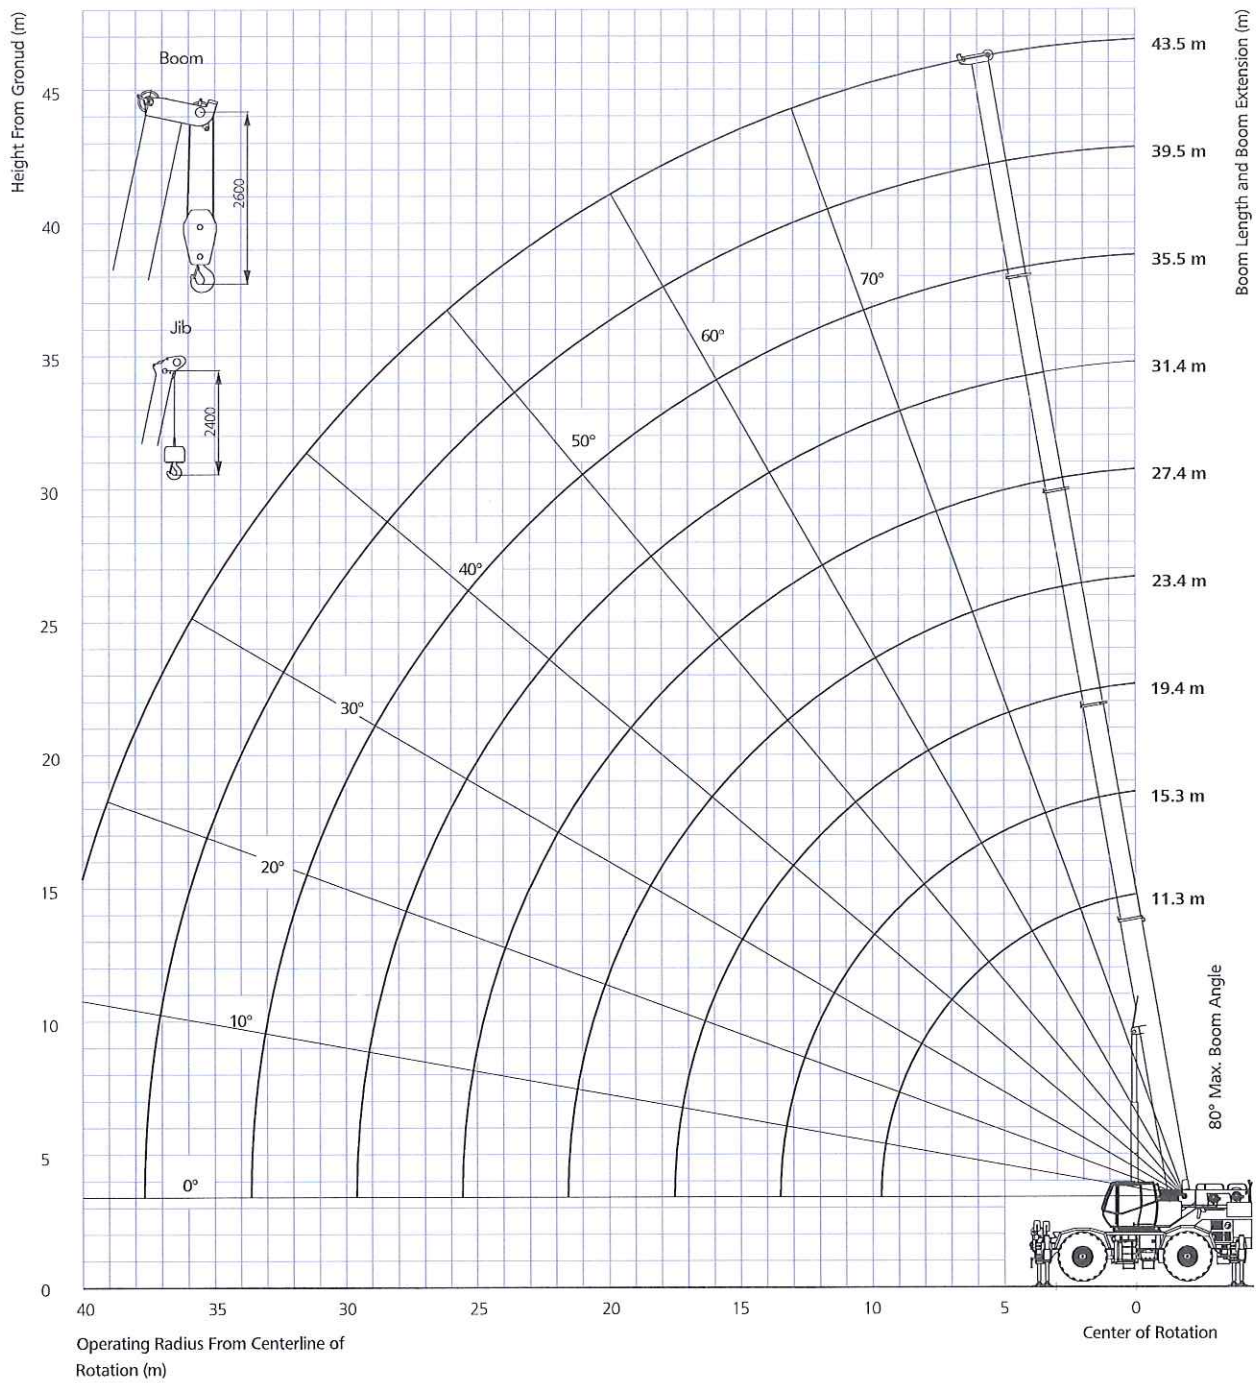

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	31.43	35.45	39.48	43.50	Radius (m)
3.0	60.00	45.00	35.00	22.00						3.0
3.5	57.00	45.00	35.00	22.00	25.00	20.00				3.5
4.0	54.00	45.00	35.00	22.00	25.00	20.00	22.50	17.05		4.0
4.5	47.80	43.00	33.00	22.00	25.00	20.00	22.50	17.05	17.50	4.5
5.0	43.00	41.00	32.00	22.00	24.50	20.00	22.00	17.05	17.50	5.0
5.5	39.00	38.00	32.00	22.00	24.20	20.00	21.50	17.05	17.50	5.5
6.0	35.50	34.70	32.00	22.00	23.80	19.50	20.50	17.05	17.50	6.0
6.5	32.50	32.00	30.50	22.00	22.30	19.00	19.80	16.30	17.50	6.5
7.0	30.00	29.70	29.00	22.00	21.50	18.50	18.80	15.70	17.50	7.0
7.5	27.80	27.50	26.00	22.00	21.00	18.00	18.00	15.00	17.50	7.5
8.0	25.80	25.00	23.50	22.00	20.00	17.50	17.20	14.50	16.50	8.0
9.0	20.00	20.00	19.50	21.70	18.00	17.00	16.50	13.50	15.00	9.0
10.0		16.00	16.00	17.80	16.00	12.50	15.00	12.50	13.50	10.0
12.0		10.90	11.00	12.80	12.00	12.00	11.80	10.70	11.00	12.0
14.0			7.70	9.80	8.50	9.50	8.80	9.35	8.60	14.0
16.0			5.50	7.50	6.00	7.80	6.80	8.05	6.90	16.0
18.0					4.50	6.50	5.20	6.55	5.60	18.0
20.0					3.40	5.30	4.10	5.35	4.40	20.0
22.0							3.15	4.45	3.30	22.0
24.0							2.45	3.65	2.50	24.0
26.0									1.90	26.0
28.0									1.50	28.0
30.0									1.35	30.0
32.0									1.00	32.0
34.0										34.0
36.0										36.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	5st boom
Number of parts of line	10	10	8	8	6	6	4	4	4	Number of parts of line

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	31.43	35.45	39.48	43.50	Radius (m)
3.0	55.00	45.00	35.00	22.00						3.0
3.5	50.00	41.00	32.50	21.00	25.00	20.00				3.5
4.0	44.40	37.00	30.50	19.80	24.00	19.00	22.50	18.50		4.0
4.5	38.00	33.50	29.00	18.80	22.50	18.00	21.50	17.20	17.50	4.5
5.0	32.00	30.00	26.50	17.50	21.50	16.50	20.80	15.00	17.20	5.0
5.5	27.00	25.50	23.50	16.20	20.80	15.00	20.40	13.80	17.00	5.5
6.0	22.50	21.50	20.00	15.00	20.00	14.20	19.80	13.20	16.50	6.0
6.5	19.00	18.00	17.50	14.20	18.00	13.50	18.00	12.80	15.80	6.5
7.0	16.00	15.50	15.20	13.50	15.40	13.00	15.50	12.40	14.80	7.0
7.5	14.00	13.80	13.00	13.00	13.50	12.50	13.80	12.00	13.50	7.5
8.0	12.00	12.00	11.00	12.40	12.20	12.00	12.50	11.50	12.20	8.0
9.0	9.50	9.50	9.60	11.20	9.80	11.00	10.00	10.60	10.00	9.0
10.0		7.40	7.60	9.70	7.80	9.50	8.00	9.20	8.30	10.0
12.0		5.00	5.00	7.20	5.30	7.00	5.40	6.80	5.50	12.0
14.0			3.40	5.40	3.70	5.30	3.90	5.20	4.00	14.0
16.0			2.20	3.80	2.60	3.70	2.80	3.70	2.90	16.0
18.0					1.80	2.70	2.00	2.80	2.10	18.0
20.0					1.20	2.10	1.50	2.20	1.60	20.0
22.0							0.90	1.70	1.10	22.0
24.0							1.30		1.40	24.0
26.0								1.00	0.90	26.0
28.0								0.90	0.90	28.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	5st boom
Min boom angle	20	25	25	20	20	20	30	20	40	Min boom angle
Number of parts of line	10	10	8	8	6	6	4	4	4	Number of parts of line


Load Chart - Telescopic Boom

Unit: t




Radius (m)	11.30	15.33	19.35	23.38	27.40	31.43	35.45	39.48	43.50	Radius (m)
3.0	30.00	30.00	25.00	22.00						3.0
3.5	24.80	24.00	23.50	20.50	20.00	20.00				3.5
4.0	18.80	18.00	17.50	18.00	17.00	17.80	16.50	17.50		4.0
4.5	15.20	14.50	13.50	15.50	14.00	15.50	14.00	15.20	14.00	4.5
5.0	12.90	12.00	11.40	13.50	11.80	13.50	12.00	13.20	12.00	5.0
5.5	11.20	10.50	10.00	11.50	10.20	11.50	10.50	11.50	10.80	5.5
6.0	9.80	9.00	8.50	10.20	9.00	10.20	9.20	10.20	9.50	6.0
6.5	8.60	8.00	7.50	8.80	7.80	8.90	8.00	9.00	8.20	6.5
7.0	7.60	7.00	6.50	7.80	7.00	7.90	7.20	8.00	7.30	7.0
7.5	6.60	6.00	5.60	7.00	6.20	7.10	6.50	7.20	6.50	7.5
8.0	5.70	5.20	5.00	6.00	5.20	6.10	5.50	6.20	5.60	8.0
9.0	4.30	4.00	3.80	4.70	4.20	4.90	4.50	5.00	4.50	9.0
10.0		3.00	2.80	3.60	3.00	3.80	3.20	3.90	3.20	10.0
12.0		1.60	1.40	2.40	1.80	2.60	2.00	2.70	2.10	12.0
14.0				1.60	1.00	1.80	1.20	1.90	1.30	14.0
16.0				1.00		1.20		1.30	0.80	16.0
18.0							0.90	0.90	0.90	18.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	5st boom
Min boom angle	20	25	45	25	45	40	55	45	55	Min boom angle
Number of parts of line	10	8	6	6	6	6	4	4	4	Number of parts of line

Jib Operating Range

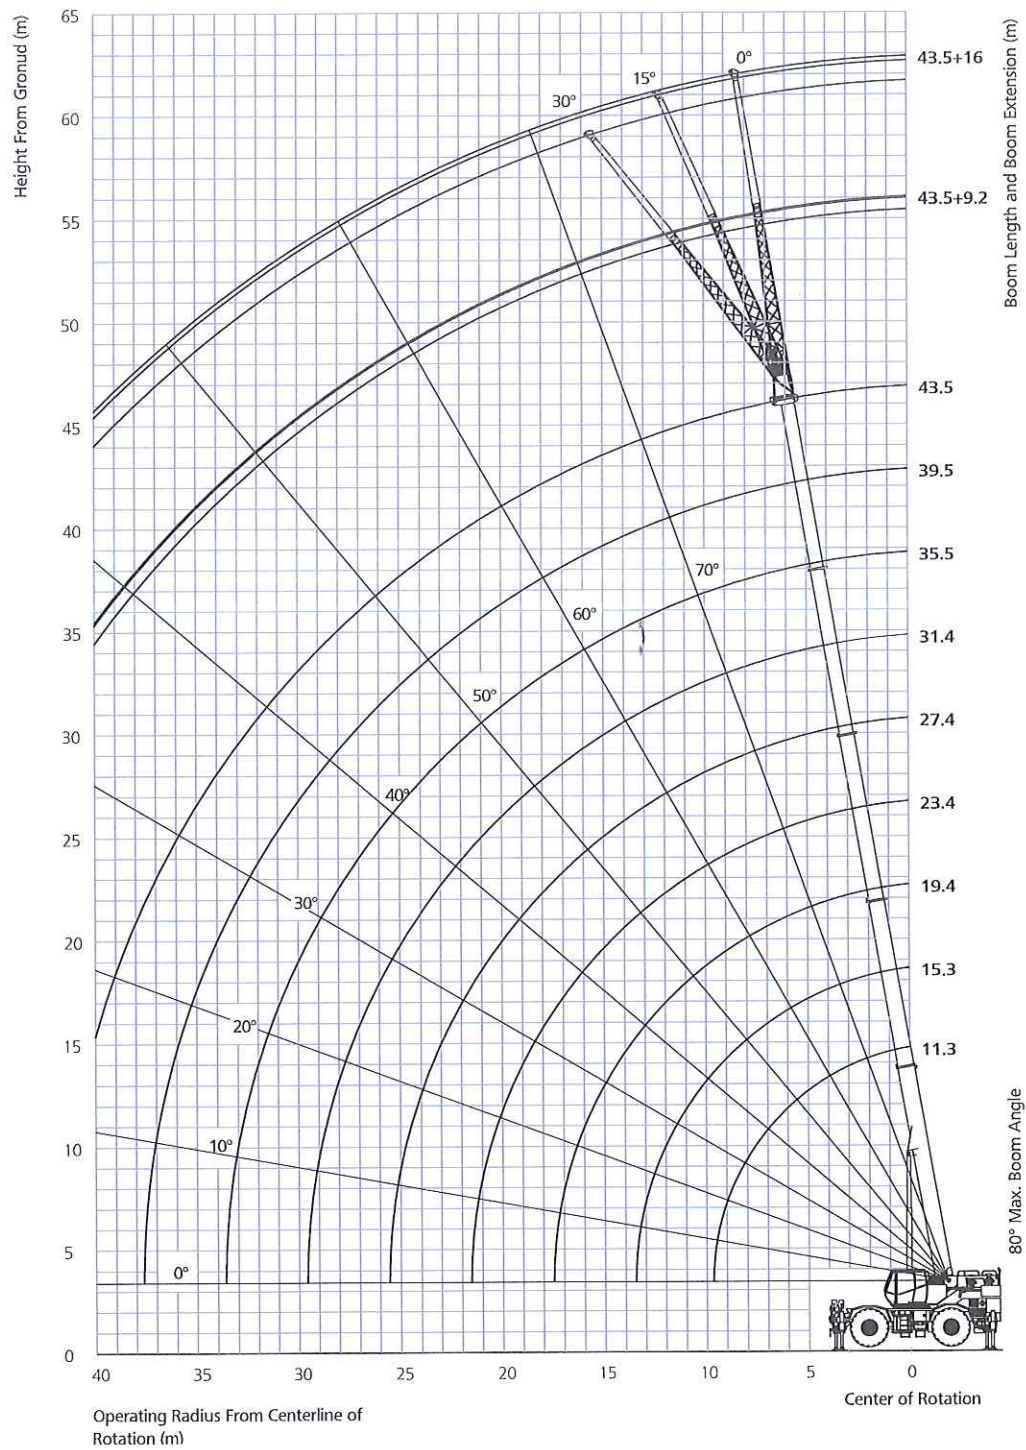

Load Chart - Fixed Jib


Unit: t



Working length of the boom	43.5m+9.2m			43.5m+16m			Working length of the boom
	0°	15°	30°	0°	15°	30°	
80	4.50	2.70	2.40	2.60	1.50	1.10	80
78	4.50	2.70	2.40	2.60	1.50	1.10	78
76	4.00	2.50	2.30	2.40	1.40	1.10	76
74	3.75	2.40	2.25	2.20	1.30	1.10	74
72	3.50	2.30	2.15	2.00	1.20	1.00	72
70	3.00	2.20	2.05	1.80	1.15	1.00	70
68	2.70	2.10	1.95	1.60	1.10	0.95	68
66	2.50	2.00	1.85	1.50	1.05	0.90	66
64	2.20	1.80	1.75	1.45	1.00	0.85	64
62	2.00	1.65	1.50	1.30	0.95	0.80	62
60	1.70	1.45	1.20	1.10	0.85	0.75	60
58	1.20	1.00	0.85	0.90	0.75	0.65	58
56	1.00	0.85	0.75	0.80	0.65	0.60	56
54	0.80	0.70	0.60	0.70	0.60		54
52	0.70	0.60	0.55				52
50	0.60						50
Min Angle(°)	48°	50°	50°	52°	52°	54°	Min Angle(°)

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	18.10	14.10	9.00			3
3.5	16.00	14.10	8.00	6.50		3.5
4	14.30	14.10	7.00	6.50		4
4.5	12.85	12.65	7.20	6.50	5.50	4.5
5	11.60	11.40	6.50	6.50	5.00	5
5.5	10.50	10.30	6.00	6.00	4.50	5.5
6	9.20	9.35	5.30	5.00	4.20	6
6.5	8.00	8.40	4.80	4.30	3.80	6.5
7	7.00	7.50	4.20	4.00	3.50	7
7.5	6.00	6.60	3.80	3.50	3.20	7.5
8	5.30	5.80	3.20	3.00	2.90	8
8.5	4.65	5.40	2.95	2.70	2.50	8.5
9	4.00	5.00	2.70	2.40	2.20	9
10		4.00	2.20	2.00	1.90	10
11			1.70	1.60	1.50	11
12				1.50	1.30	12
14					1.00	14
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	20.00	16.00	15.00			3
3.5	20.00	16.00	15.00	11.00		3.5
4	20.00	16.00	14.00	11.00	10.00	4
4.5	17.50	15.00	13.00	11.00	10.00	4.5
5	14.50	13.00	12.00	11.00	10.00	5
5.5	12.00	11.00	11.00	10.00	10.00	5.5
6	10.30	10.00	10.00	9.50	9.50	6
6.5	9.10	9.00	8.80	9.00	9.20	6.5
7	7.80	7.90	8.00	8.00	8.00	7
7.5	6.80	6.90	7.00	7.20	7.50	7.5
8	6.00	6.00	6.00	6.50	7.10	8
8.5	5.20	5.00	5.00	6.00	6.30	8.5
9	4.50	4.50	4.00	5.00	5.50	9
10		3.50	3.00	4.00	4.20	10
11			2.00	3.30	3.80	11
12			1.00	2.80	3.00	12
14				1.80	2.00	14
16				1.00		16
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines

Load Chart - Telescopic Boom

Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	12.00	10.50	10.0			3
3.5	12.00	10.50	10.0			3.5
4	10.00	10.00	9.0	8.00		4
4.5	8.60	8.00	8.0	6.50	5.50	4.5
5	7.00	6.50	6.0	5.70	5.50	5
5.5	5.80	4.80	4.5	5.00	5.50	5.5
6	4.30	3.00	3.0	4.00	5.50	6
6.5	3.00	2.50	2.5	3.00	3.50	6.5
7	2.50	2.00	2.0	2.50	3.00	7
7.5	2.00	1.50	1.5	1.70	2.00	7.5
8	1.50	1.50	1.5	1.70	2.00	8
8.5		1.00	1.0	1.20	1.50	8.5
9					1.00	9
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines
