

SRC-RT-060-004



BUREAU
VERITAS



CERTIFICATE OF TEST AND THOROUGH EXAMINATION OF MOBILE CRANE

Cert. No.: 1624495	Date of Examination: 19/03/2024	Sticker No.: Load test
--------------------	---------------------------------	------------------------

Name & address of owner of the equipment		SUDHIR EQUIPMENT RENTAL CO.
Inspection requested by		SUDHIR EQUIPMENT RENTAL CO.
Place of inspection		DMM YARD
Type of inspection		TEST & THOROUGH EXAMINATION
Relevant regulation / Standard		ASME B30.5
Date of previous inspection / load test		19/03/2024Not applicable
Identification & Description of the Equipment	Manufacturer name	SANY
	Equipment Type	RT MOBILE CRANE
	Nature of power	DEISEL POWERED
	Model / Year	SRC600C
	Serial number	A0032
	Owner ID / Registration number	SRC-RT-060-004
	Rated Capacity (maximum)	60 t
	Present Configuration	Main hoist current capacity: 60 t with 6 falls
		Auxiliary hoist current capacity: 5.6 t with 1
	Radius (Mini / Max)	Minimum: 3 m; Maximum: 36 m
	Length of Boom	Minimum: 11.3 m; Maximum:43.5 m
	Counterweight (mass)	Standard from Manufacturer
	Wire rope specification	21 mm
Complementary devices	N/A	

Description of test: Visual inspection was carried out, followed by full functional testing. Note: "This certificate does not cover the use of the equipment for Personnel/Man riding purposes".	Length of boom (m)	Radius (m)	Reeving (No. of falls)	Test Load	Safe Working Load
	15.3 m	7 m	6 falls	27500 kg	27500 kg
	19.3 m	10 m	6 falls	16000 kg	16000 kg
	27.4 m	18 m	6 falls	5200 kg	5200 kg

Result of Examination:

The above mentioned equipment has been found satisfactory at the time of inspection and is considered to be safe for further use, subject to continuous maintenance being applied and qualified operator being employed.

This is to certify that the Competent Person did attend at the said premises on said date to witness proof load test and/or to carry out thorough examination of the equipment described herein and that all particulars described above were correct at the time of examination. This Certificate becomes void in case of any major repair, modification and / or alteration being un-authorized by issuer of hereof.

Next Proof Load Test Due: or After Major Repair/Modifications	Next Inspection Due is on or before: 18/03/2025
---	---

Issued at Al Khobar on 31/03/2024

Inspector to Bureau Veritas
Signature:

Name: Mohamed OMARA
Position: Senior Inspector



Reviewed by
Signature:

Name: Abdullah SHEHRI
Position: Operations Manager

The technical conclusions thus expressed may have to be reconsidered in light of any modifications or alterations that would invalidate the data shown in the present certificate. These conclusions would become null & void should Bureau Veritas not be kept informed of such modifications or alterations with specific reference to the present certificate.

Any person not a party to the contract pursuant to which this document is delivered may not assert a claim against Bureau Veritas for any liability arising out of errors or omissions which may be contained in said document, or for errors of judgement, fault or negligence committed by the personnel of the Society or of its Agents in the establishment or issuance of this document, and in connection with any activities for which it may provide.

This is NOT an indication that the item(s) is (are) fit for any specific purpose and does not release the manufacturer, supplier and any party from their respective duty, guarantee, obligation and/or indemnity relating to, without limitation patents, workmanship, materials, safety, performance in operation and/or reliability.





**BUREAU
VERITAS**



4.11 Traveling Brake	Satisfactory	
4.12 Guards for moving parts	Satisfactory	
4.13 Motor	Satisfactory	
4.14 Gear box	Satisfactory	
5. LIFTING SYSTEM		
5.1 Wire rope / chain	Satisfactory	
5.2 Wire/chain rope end termination	Satisfactory	
5.3 Drum, pulley, return pulley	Satisfactory	
5.4 Hooks & hook blocks	Satisfactory	
5.5 Other load handling devices	Satisfactory	
6. ENERGY		
6.1 Main switch locking	Satisfactory	
6.2 Equipment and cabling	Satisfactory	
6.3 Protection of live parts/enclosure	Satisfactory	
6.4 Lighting of the crane/site	Satisfactory	
7. CABIN / CONTROL STATION		
7.1 Structure	Satisfactory	
7.2 Visibility / windows	Satisfactory	
7.3 Heating / AC system	Satisfactory	
7.4 Seat	Satisfactory	
7.5 Fire extinguisher	Satisfactory	
7.6 Identification of the controls	Satisfactory	
7.7 Control dead man type	Satisfactory	
7.8 General stopping device by key	Satisfactory	
7.9 Emergency stop button	Satisfactory	
7.10 Level indicator	Satisfactory	
7.11 Angle Indicator	Satisfactory	
7.12 Horn	Satisfactory	
7.13 Traffic lights	Satisfactory	
7.14 Direction Indicators	Satisfactory	
8. SAFETY DEVICES		



BUREAU
VERITAS



8.1 Hoisting limiter/Anti Two Blocks	Satisfactory	
8.2 Luffing limiter	Not applicable	
8.3 Telescopic limiter	Satisfactory	
8.4 Slewing limiter	Satisfactory	
8.5 Load limiter	Satisfactory	
8.6 Level limiter	Satisfactory	
8.7 Rated capacity indicator (RCI) / ASLI	Satisfactory	
8.8 None return valve on piston	Satisfactory	
8.9 Other limiter or indicator	Satisfactory	
9. MISCELLANEOUS REQUIREMENTS		
9.1 Maker plate	Satisfactory	
9.2 Load chart	Satisfactory	
9.3 Wire rope certificate	Satisfactory	
9.4 General Safety Requirements	Satisfactory	
Notes : - Maintain proper housekeeping & preventive maintenance.		
Next Proof Load Test Due: or After Major Repair/Modifications		Next Inspection Due is on or before: 18/03/2025

Inspector to Bureau Veritas
Signature:



Name: Mohamed OMARA
Position: Senior Inspector



الرقم المرجعي : 1713356944363

تاريخ إصدار القائمة : 2024-04-17

رقم العميل: 7016158334

اسم العميل: شركة سودهير لتأجير المعدات

العدد الحقيقي لمجموع المركبات 63												
اسم المستخدم الفعلي	هوية المستخدم الفعلي	حالة التأمين	تاريخ انتهاء رخصة السير	تاريخ الملكية	تاريخ الأساسي	اللون الأساسي	رقم الهيكل	رقم التسلسلي	الرقم الصنع	سنة الصنع	الطراز	الماركة
MAJID MEWA QASIM	2064588540	ساري	1448-04-08	1442-04-08	1442-04-08	أزرق	LFCNN35DXL2000151	78490810	2020	2020	كرين	سالي
		ساري	1447-03-16	1438-03-16	1438-03-16	رصاصي	JN1BT2MU8GW005059	724237510	2016	2016	اكس تيرل	نيسان
		ساري	1447-05-11	1444-05-11	1444-05-11	أبيض	MR0DB8CD2H0115608	264305910	2017	2017	يخب غمارتين	تويوتا
		ساري	1447-12-02	1444-12-02	1444-12-02	فضي	MZBGB8T44PN082328	220949910	2023	2023	كارنس واجن	كيا
		ساري	1448-01-13	1445-01-13	1445-01-13	أبيض	RKLB20DE884001253	71630020	2024	2024	كوروبل	تويوتا
		ساري	1448-04-07	1442-04-07	1442-04-07	أزرق	LFCNN35D2L2000032	395290810	2020	2020	كرين	سالي
		ساري	1445-12-22	1442-12-22	1442-12-22	برتقالي	FDB08-1130-01647	593355810	2019	2019	رافعة	دوسان
		ساري	1447-03-16	1444-03-16	1444-03-16	أبيض	JE3AB36U9HU712807	599093910	2017	2017	لانسر	متسوبيشي
		ساري	1448-04-07	1442-04-07	1442-04-07	أزرق	LFCNN35D8L2000049	33290810	2020	2020	رافعة شوكيه	معدم
		ساري	1445-04-04	1442-04-04	1442-04-04	أزرق	LFCNN35DXL2000036	224090810	2020	2020	كرين	سالي
		ساري	1447-12-04	1444-12-04	1444-12-04	أبيض	MPAER33T7PT006557	96069910	2023	2023	يخب غمارتين	ايسوزو
		ساري	1446-10-22	1443-10-22	1443-10-22	برتقالي	011002P8148	427901910	2022	2022	رافعة شوكية	هيلي
		ساري	1447-02-23	1444-02-23	1444-02-23	أبيض	KMHD741F6HU254660	207143910	2017	2017	الترا	هونداي
MUSTAFA ABDUL	2520037231	ساري	1447-05-04	1444-05-04	1444-05-04	أسود	MMBNGV549NH014296	866684910	2022	2022	يخب غمارتين	متسوبيشي
		ساري	1447-07-21	1444-07-21	1444-07-21	برتقالي	010702T6063	384256910	2023	2023	رافعة شوكية	هيلي
		ساري	1446-08-16	1440-08-16	1440-08-16	أبيض	JTEBU9FJ3KK166601	315611710	2019	2019	برادو	تويوتا

NO.BV-23-1727



**BUREAU
VERITAS**
Tel.: 013 822 1071
Fax: 013 822 1072



EQUIP NO.: SRC-RT-60-004

EQUIP S. N. : A0032


DATE INSPECTED : 16/04/2024

NEXT INSPECTION DATE : 15/07/2024

INSPECTED BY : Mohamed OMARA


**SA INSPECTION DEPARTMENT APPROVED CONTRACTOR
AGENCIES**

Boom Operating Range

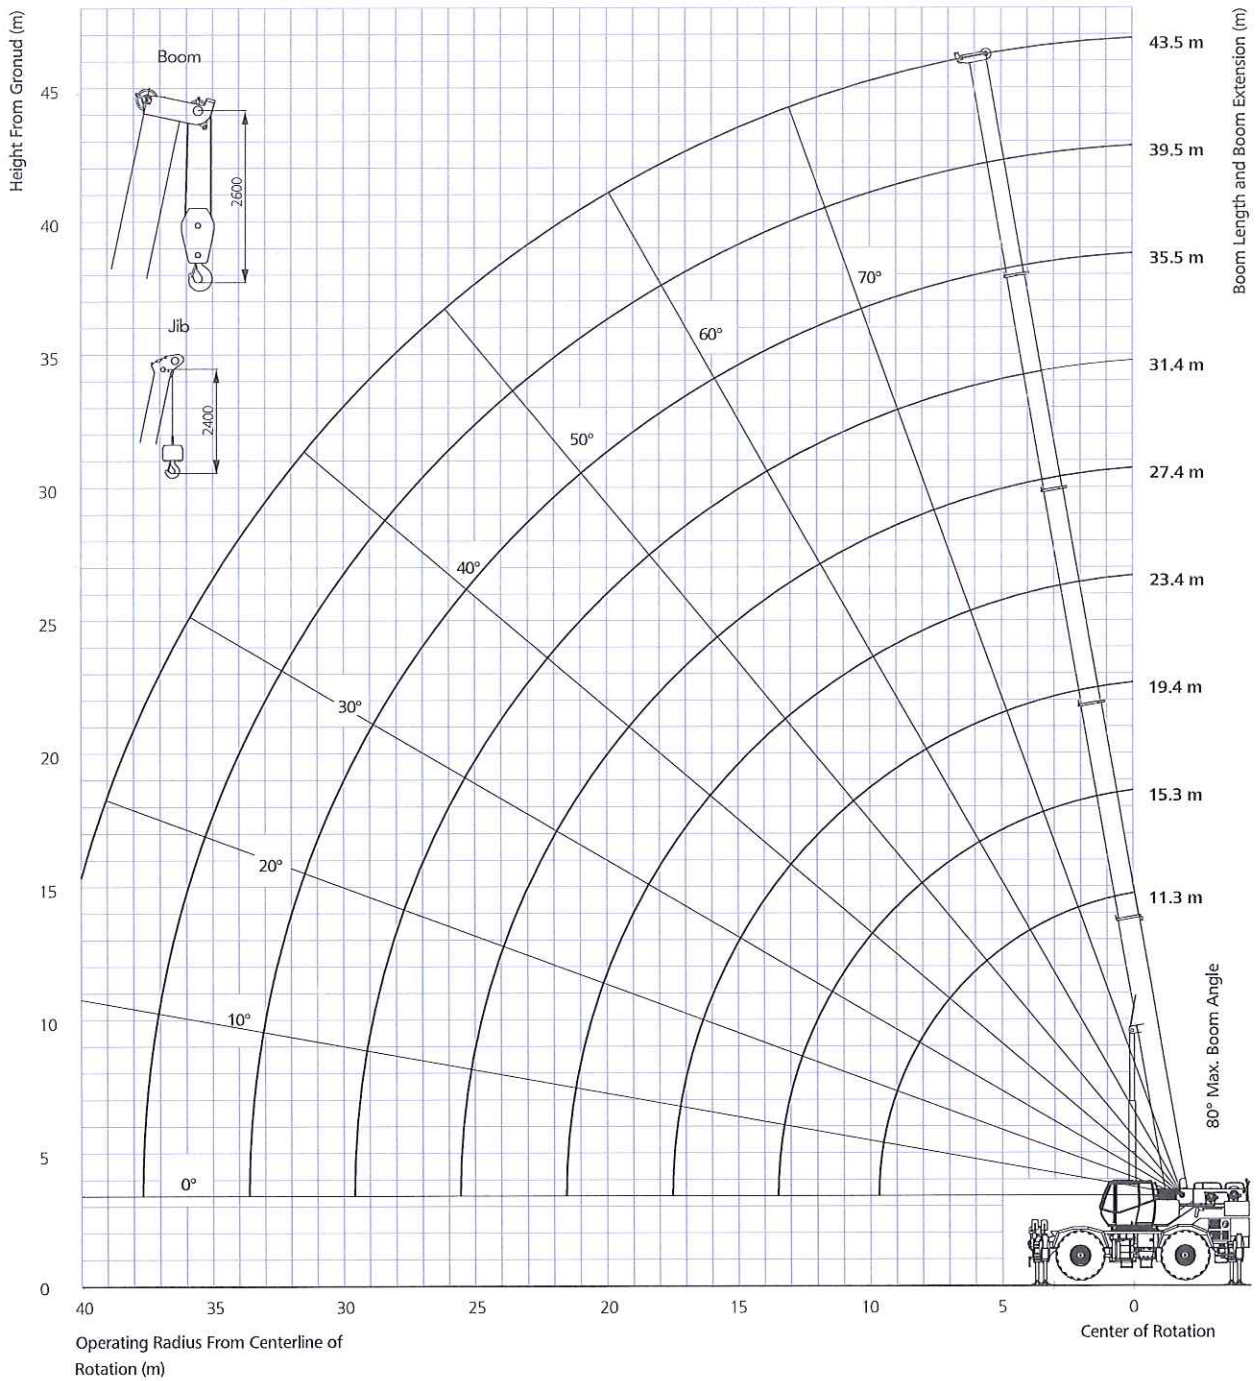

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35		23.38		27.40		31.43		35.45		39.48		43.50	Radius (m)
3.0	60.00	45.00	35.00	22.00												3.0
3.5	57.00	45.00	35.00	22.00	25.00	20.00										3.5
4.0	54.00	45.00	35.00	22.00	25.00	20.00	22.50	17.05								4.0
4.5	47.80	43.00	33.00	22.00	25.00	20.00	22.50	17.05	17.50	15.00						4.5
5.0	43.00	41.00	32.00	22.00	24.50	20.00	22.00	17.05	17.50	15.00						5.0
5.5	39.00	38.00	32.00	22.00	24.20	20.00	21.50	17.05	17.50	15.00	15.50	11.00				5.5
6.0	35.50	34.70	32.00	22.00	23.80	19.50	20.50	17.05	17.50	14.50	14.50	11.00				6.0
6.5	32.50	32.00	30.50	22.00	22.30	19.00	19.80	16.30	17.50	14.00	14.00	11.00	12.50	10.00		6.5
7.0	30.00	29.70	29.00	22.00	21.50	18.50	18.80	15.70	17.50	13.50	14.00	11.00	12.00	10.00	9.50	7.0
7.5	27.80	27.50	26.00	22.00	21.00	18.00	18.00	15.00	17.50	13.00	13.00	11.00	11.50	10.00	9.50	7.5
8.0	25.80	25.00	23.50	22.00	20.00	17.50	17.20	14.50	16.50	12.50	12.50	11.00	11.00	10.00	9.50	8.0
9.0	20.00	20.00	19.50	21.70	18.00	17.00	16.50	13.50	15.00	12.00	12.00	10.30	10.50	10.00	9.30	9.0
10.0		16.00	16.00	17.80	16.00	12.50	15.00	12.50	13.50	11.00	11.50	9.60	10.00	9.60	9.00	10.0
12.0		10.90	11.00	12.80	12.00	12.00	11.80	10.70	11.00	10.00	10.00	8.60	9.00	9.10	8.30	12.0
14.0			7.70	9.80	8.50	9.50	8.80	9.35	8.60	8.60	8.50	7.80	8.00	8.60	8.00	14.0
16.0			5.50	7.50	6.00	7.80	6.80	8.05	6.90	7.20	7.10	6.75	7.30	7.60	7.35	16.0
18.0					4.50	6.50	5.20	6.55	5.60	6.20	5.70	6.05	6.00	6.20	5.80	18.0
20.0					3.40	5.30	4.10	5.35	4.40	5.20	4.50	5.25	4.80	4.90	4.70	20.0
22.0							3.15	4.45	3.30	4.40	3.55	4.55	3.70	4.15	3.80	22.0
24.0							2.45	3.65	2.50	3.60	2.85	3.75	2.90	3.35	3.10	24.0
26.0									1.90	3.10	2.25	3.25	2.30	2.85	2.50	26.0
28.0									1.50	2.60	1.75	2.75	1.90	2.35	2.00	28.0
30.0											1.35	2.35	1.50	1.95	1.60	30.0
32.0											1.00	1.95	1.20	1.55	1.25	32.0
34.0													0.90	1.25	0.95	34.0
36.0													0.70	1.05		36.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	0%	100%	0%	100%	50%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	84%	66%	100%	84%	100%	100%	5st boom
Number of parts of line	10	10	8	8	6	6	4	4	4	4	4	4	4	4	3	Number of parts of line

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	31.43	35.45	39.48	43.50	Radius (m)
3.0	55.00	45.00	35.00	22.00						3.0
3.5	50.00	41.00	32.50	21.00	25.00	20.00				3.5
4.0	44.40	37.00	30.50	19.80	24.00	19.00	22.50	18.50		4.0
4.5	38.00	33.50	29.00	18.80	22.50	18.00	21.50	17.20	17.50	4.5
5.0	32.00	30.00	26.50	17.50	21.50	16.50	20.80	15.00	17.20	5.0
5.5	27.00	25.50	23.50	16.20	20.80	15.00	20.40	13.80	17.00	5.5
6.0	22.50	21.50	20.00	15.00	20.00	14.20	19.80	13.20	16.50	6.0
6.5	19.00	18.00	17.50	14.20	18.00	13.50	18.00	12.80	15.80	6.5
7.0	16.00	15.50	15.20	13.50	15.40	13.00	15.50	12.40	14.80	7.0
7.5	14.00	13.80	13.00	13.00	13.50	12.50	13.80	12.00	13.50	7.5
8.0	12.00	12.00	11.00	12.40	12.20	12.00	12.50	11.50	12.20	8.0
9.0	9.50	9.50	9.60	11.20	9.80	11.00	10.00	10.60	10.00	9.0
10.0		7.40	7.60	9.70	7.80	9.50	8.00	9.20	8.30	10.0
12.0		5.00	5.00	7.20	5.30	7.00	5.40	6.80	5.50	12.0
14.0			3.40	5.40	3.70	5.30	3.90	5.20	4.00	14.0
16.0			2.20	3.80	2.60	3.70	2.80	3.70	2.90	16.0
18.0					1.80	2.70	2.00	2.80	2.10	18.0
20.0					1.20	2.10	1.50	2.20	1.60	20.0
22.0							0.90	1.70	1.10	22.0
24.0								1.30		24.0
26.0								1.40	0.90	26.0
28.0								1.00		28.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	5st boom
Min boom angle	20	25	25	20	20	20	30	20	40	Min boom angle
Number of parts of line	10	10	8	8	6	6	4	4	4	Number of parts of line


Load Chart - Telescopic Boom

Unit: t




Radius (m)	11.30	15.33	19.35	23.38	27.40	31.43	35.45	39.48	43.50	Radius (m)
3.0	30.00	30.00	25.00	22.00						3.0
3.5	24.80	24.00	23.50	20.50	20.00	20.00				3.5
4.0	18.80	18.00	17.50	18.00	17.00	17.80	16.50	17.50		4.0
4.5	15.20	14.50	13.50	15.50	14.00	15.50	14.00	15.20	14.00	4.5
5.0	12.90	12.00	11.40	13.50	11.80	13.50	12.00	13.20	12.00	5.0
5.5	11.20	10.50	10.00	11.50	10.20	11.50	10.50	11.50	10.80	5.5
6.0	9.80	9.00	8.50	10.20	9.00	10.20	9.20	10.20	9.50	6.0
6.5	8.60	8.00	7.50	8.80	7.80	8.90	8.00	9.00	8.20	6.5
7.0	7.60	7.00	6.50	7.80	7.00	7.90	7.20	8.00	7.30	7.0
7.5	6.60	6.00	5.60	7.00	6.20	7.10	6.50	7.20	6.50	7.5
8.0	5.70	5.20	5.00	6.00	5.20	6.10	5.50	6.20	5.60	8.0
9.0	4.30	4.00	3.80	4.70	4.20	4.90	4.50	5.00	4.50	9.0
10.0		3.00	2.80	3.60	3.00	3.80	3.20	3.90	3.20	10.0
12.0		1.60	1.40	2.40	1.80	2.60	2.00	2.70	2.10	12.0
14.0				1.60	1.00	1.80	1.20	1.90	1.30	14.0
16.0				1.00		1.20		1.30	0.80	16.0
18.0							0.90		0.90	18.0
2st boom	0%	50%	100%	0%	100%	0%	100%	0%	100%	2st boom
3st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	3st boom
4st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	4st boom
5st boom	0%	0%	0%	33%	17%	50%	33%	66%	50%	5st boom
Min boom angle	20	25	45	25	45	40	55	45	55	Min boom angle
Number of parts of line	10	8	6	6	6	6	4	4	4	Number of parts of line

Jib Operating Range

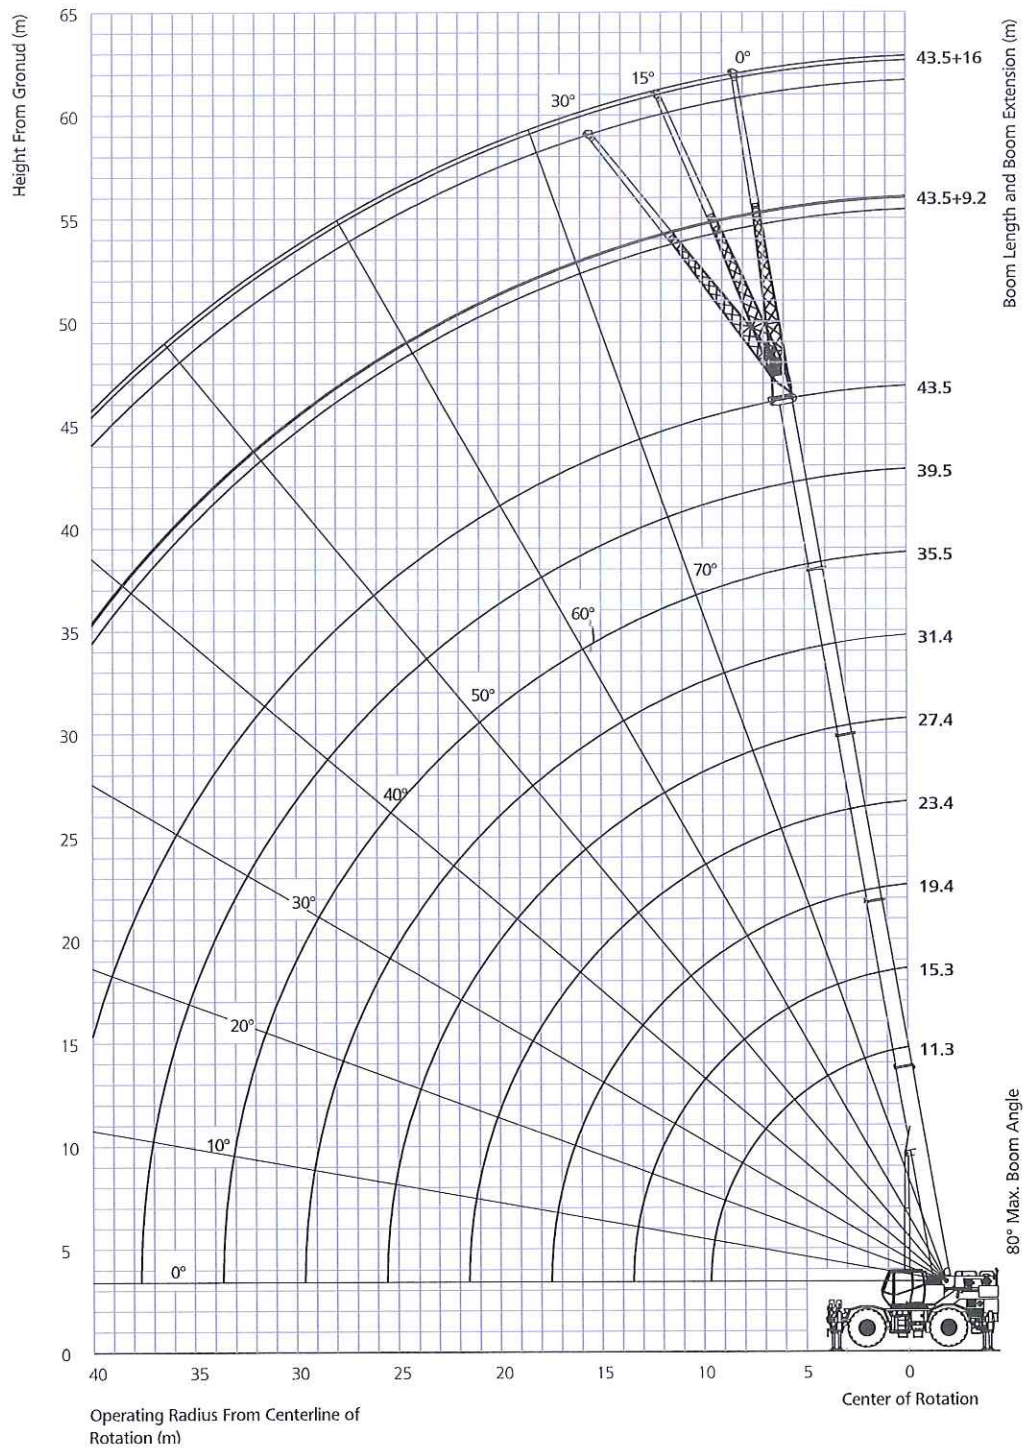

Load Chart - Fixed Jib


Unit: t



Working length of the boom	43.5m+9.2m			43.5m+16m			Working length of the boom
	0°	15°	30°	0°	15°	30°	
80	4.50	2.70	2.40	2.60	1.50	1.10	80
78	4.50	2.70	2.40	2.60	1.50	1.10	78
76	4.00	2.50	2.30	2.40	1.40	1.10	76
74	3.75	2.40	2.25	2.20	1.30	1.10	74
72	3.50	2.30	2.15	2.00	1.20	1.00	72
70	3.00	2.20	2.05	1.80	1.15	1.00	70
68	2.70	2.10	1.95	1.60	1.10	0.95	68
66	2.50	2.00	1.85	1.50	1.05	0.90	66
64	2.20	1.80	1.75	1.45	1.00	0.85	64
62	2.00	1.65	1.50	1.30	0.95	0.80	62
60	1.70	1.45	1.20	1.10	0.85	0.75	60
58	1.20	1.00	0.85	0.90	0.75	0.65	58
56	1.00	0.85	0.75	0.80	0.65	0.60	56
54	0.80	0.70	0.60	0.70	0.60		54
52	0.70	0.60	0.55				52
50	0.60						50
Min Angle(°)	48°	50°	50°	52°	52°	54°	Min Angle(°)

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	18.10	14.10	9.00			3
3.5	16.00	14.10	8.00	6.50		3.5
4	14.30	14.10	7.00	6.50		4
4.5	12.85	12.65	7.20	6.50	5.50	4.5
5	11.60	11.40	6.50	6.50	5.00	5
5.5	10.50	10.30	6.00	6.00	4.50	5.5
6	9.20	9.35	5.30	5.00	4.20	6
6.5	8.00	8.40	4.80	4.30	3.80	6.5
7	7.00	7.50	4.20	4.00	3.50	7
7.5	6.00	6.60	3.80	3.50	3.20	7.5
8	5.30	5.80	3.20	3.00	2.90	8
8.5	4.65	5.40	2.95	2.70	2.50	8.5
9	4.00	5.00	2.70	2.40	2.20	9
10		4.00	2.20	2.00	1.90	10
11			1.70	1.60	1.50	11
12				1.50	1.30	12
14					1.00	14
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines

Load Chart - Telescopic Boom


Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	20.00	16.00	15.00			3
3.5	20.00	16.00	15.00	11.00		3.5
4	20.00	16.00	14.00	11.00	10.00	4
4.5	17.50	15.00	13.00	11.00	10.00	4.5
5	14.50	13.00	12.00	11.00	10.00	5
5.5	12.00	11.00	11.00	10.00	10.00	5.5
6	10.30	10.00	10.00	9.50	9.50	6
6.5	9.10	9.00	8.80	9.00	9.20	6.5
7	7.80	7.90	8.00	8.00	8.00	7
7.5	6.80	6.90	7.00	7.20	7.50	7.5
8	6.00	6.00	6.00	6.50	7.10	8
8.5	5.20	5.00	5.00	6.00	6.30	8.5
9	4.50	4.50	4.00	5.00	5.50	9
10		3.50	3.00	4.00	4.20	10
11			2.00	3.30	3.80	11
12			1.00	2.80	3.00	12
14				1.80	2.00	14
16				1.00		16
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines

Load Chart - Telescopic Boom

Unit: t



Radius (m)	11.30	15.33	19.35	23.38	27.40	Radius (m)
3	12.00	10.50	10.0			3
3.5	12.00	10.50	10.0			3.5
4	10.00	10.00	9.0	8.00		4
4.5	8.60	8.00	8.0	6.50	5.50	4.5
5	7.00	6.50	6.0	5.70	5.50	5
5.5	5.80	4.80	4.5	5.00	5.50	5.5
6	4.30	3.00	3.0	4.00	5.50	6
6.5	3.00	2.50	2.5	3.00	3.50	6.5
7	2.50	2.00	2.0	2.50	3.00	7
7.5	2.00	1.50	1.5	1.70	2.00	7.5
8	1.50	1.50	1.5	1.70	2.00	8
8.5		1.00	1.0	1.20	1.50	8.5
9					1.00	9
1st cylinder	0%	0%	0%	0%	0%	1st cylinder
2sr cylinder	0%	17%	33%	50%	67%	2sr cylinder
Parts of lines	6	6	6	6	6	Parts of lines
