



الشركة العالمية لخدمات التفتيش المحدودة
UNIVERSAL INSPECTION CO. LTD.

NDT DIVISION

Business Executive Centre, P.O.Box # 2072, Jubail -31951, Kingdom of Saudi Arabia.
Tel. : 00966 3 344 8882 / Fax : 00966 3 344 8881 / Email : info@ui.com.sa / Website : www.ui.com.sa

MAGNETIC PARTICLE EXAMINATION REPORT

Report NO.:	INSPECTION DATE:	NEXT INSPECTION DATE	Page 1 of 1
MPI-JUB-26-1818	26/08/2026	25/08/2027	

Client: SUDHIR RENTAL EQUIPMENT		Location: DAMMAM	
Reference Code: AWS D1.1		Procedure No. with Rev.: ASTM E -709	
Surface Temperature: 39°C	Surface Condition: SMOOTH	UV Light Intensity: N/A	White Light Intensity: >100FC

INSPECTION MEDIUM MAKE

Particle Mfg.	Particle P/N.	Batch No.	Color.	White Paint Mfg.:	White Paint P/N:	Batch No.
MR CHEMIE	MR76S	2402005	BLACK	MR CHEMIE	MR72	2410052

METHOD DESCRIPTION


Visible Method ☒	Dry ☐	Magnetic Current Used			Magnetic Field Direction		Demagnetization		
Fluorescent Method ☐	Wet ☒	AC ☐	DC ☐	PER. ☒	Circular Longitudinal	☐ ☒	Yes ☒	No ☐	Amp.:

MPE EQUIPMENT DETAILS

Yoke Mfg.:	PARKER	Due Date of Yoke:	3-Sep-26	Portable ☒	Prod ☐	Clamps ☐
Model:	PM-50	Due Date of Lux meter	23-Mar-27	Mobile ☐	Coil ☐	Leeches ☐
Sr.No:	6117	Due Date of UV light	N/A	Stationary ☐	Yoke ☒	C.C ☐

FIELD OF APPLICATION

Piping ☐	Raw Material ☐	Bevel ☐	1st Pass ☐	Final Pass ☐
Tank/Silos ☐	Equipment ☒	Before PWHT ☐	After Load Test ☒	After Hydro ☐

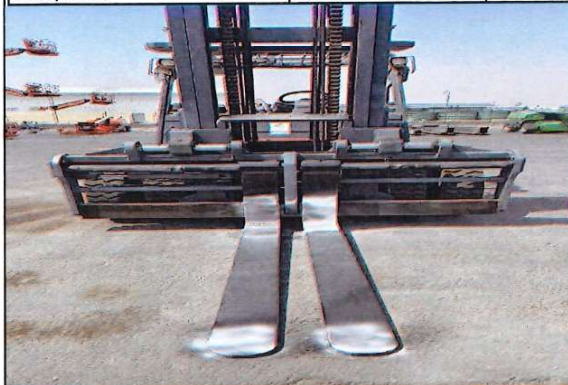

QTY.	ID. NO.	DESCRIPTION	Exam Result		Remarks
			Accept	Reject	
1	SIOFLT-026	FORKLIFT SWL- 10TON	Accept	--	--

Sketch/Description:

The above mentioned the forks are tested by Magnetic Particle Test (MPT) method and No relevant indication observed. Job is Acceptable as per code, Refer above Image of Testing.

Tested By: Technician/Inspector:	Reviewed By: Tech. Man./D.Tech. Man./Competant Person	Approved By : Owner/Consultant/T.P.I
Name	Name	Name
Reporting Date: 26-08-2026	Date	Date

