

## OWNERSHIP CERTIFICATE

To Whom It May Concern

This is to certify that the following equipment listed below is the sole property of Sudhir Equipment Rental Company:

|                           |                         |
|---------------------------|-------------------------|
| <b>Equipment</b>          | <b>Crane</b>            |
| <b>Brand / Make</b>       | <b>SANY</b>             |
| <b>Asset ID</b>           | <b>SRC-STC-060-020</b>  |
| <b>Model Number</b>       | <b>STC600T5</b>         |
| <b>Serial Number</b>      | <b>TC2060CE0540</b>     |
| <b>Capacity</b>           | <b>60 TON</b>           |
| <b>Type</b>               | <b>Sany Truck Crane</b> |
| <b>Manufacturing Year</b> | <b>2024</b>             |

This certification is issued to confirm the ownership status of the aforementioned equipment. Sudhir Equipment Rental Company holds full legal ownership rights over the listed equipment and retains all associated benefits and responsibilities. Should there be any queries or requests for verification regarding the ownership of the mentioned equipment, please do not hesitate to contact us at : [Info@sudhirrentals.com](mailto:Info@sudhirrentals.com)

Sincerely,

Ajay Koul

General Manager

Sudhir Equipment Rental Company



KINGDOM OF SAUDI ARABIA  
MINISTRY OF INTERIOR

رخصة سير  
VEHICLES REGISTRATION

المملكة العربية السعودية  
وزارة الداخلية

المالك شركة سودهير لتأجير المعدات شركة الشخص الواحد

المستخدم

هوية المالك ٧٠١٦١٥٨٣٣٤

رقم الهيكل LFCNNF5P7P3200514

رقم اللوحة ٣٧٨٢ ا ا ا

نوع التسجيل اشغال عامة

طراز المركبة كرين

حمولة المركبة ١

سنة الصنع ٢٠٢٤

ماركة المركبة ساني

وزن المركبة ٤٢٥٠٠

اللون ابيض / ابيض

الرقم التسلسلي ٧١٨٢٧٩٠٢٠





بروج للتأمين التعاوني  
Buruj Cooperative Insurance

### شهادة التأمين - CERTIFICATE OF INSURANCE

|                                      |   |                                 |   |                      |
|--------------------------------------|---|---------------------------------|---|----------------------|
| Policy Holder Name                   | : | Sudhir Equipment Rental Company | : | اسم حامل الوثيقة     |
| Policy Number                        | : | 01/CPM/ 2025/000002             | : | رقم الوثيقة          |
| Policy Period                        | : | 05/04/2025 to 04/04/2026        | : | فترة الوثيقة         |
| Description of Machinery / Equipment | : | SANY-CRANES-STC600T5            | : | وصف المعدة/ال لة     |
| Chassis / Serial No.                 | : | TC2060CE0540                    | : | رقم الهيكل/ التسلسلي |
| Year of Manufacturing                | : | 2024                            | : | سنة الصنع            |
| Asset ID No.                         | : | SRC-STC-060-020                 | : | رقم ال صل            |
| Location                             | : | Kingdom of Saudi Arabia.        | : | الموقع               |

BURUJ Cooperative Insurance Company certifies that above client is holding a Machinery/Equipment Insurance Policy for the above-mentioned Equipment in accordance with the above-mentioned Insurance Policy.

**With effect from:** 05/04/2025 to 04/04/2026

This Certificate has been issued upon Insured's request as per all terms and conditions, exclusions, warranties mentioned in the policy.

تشهد شركة بروج للتأمين التعاوني بأن السادة أعل ه مؤمنين لديها تأمين المكان/المعدات المذكورة أعل ه وذلك حسب وثيقة التأمين المذكورة أعل ه

والتي يبدأ تاريخ سريانها من ٢٠٢٥/٠٤/٠٥ إلى ٢٠٢٦/٠٤/٠٤

تم إصدار هذه الشهادة بناءً على طلب المؤمن له وذلك حسب الشروط وال استثناءات وال شتراطات المذكورة في الوثيقة.

#### Important Notices:

1. This Certificate does not pay any fines, penalties, bonds or cautions that may be imposed.
2. Original certificates are only accepted.
3. Due to the importance of correct information being stated in this certificate, kindly examine the document carefully and advise the Company of any difference.
4. In the event of changes in the above information, kindly contact +966-11-2938383

#### مل حظات هامة:

- ١) ل تطبق هذه الشهادة التأمين على الغرامات والعقوبات المالية بما في ذلك المخالفات أو الضمانات أو الكفالت التي قد تقرر.
- ٢) تقبل الشهادة ال صلية فقط.
- ٣) نظراً ل همية صحة البيانات الخاصة بكم في هذه الشهادة، الرجاء التأكد منها وإشعار الشركة في حالة وجود أي اختل فات.
- ٤) عند الحاجة إلى تعديل البيانات أعل ه يرجى ال اتصال على شركة بروج للتأمين التعاوني ٢٩٣٨٣٨٣-١١-٩٦٦+



**BURUJ Cooperative Insurance Company**

P.O. Box 51855, Riyadh 11553,  
National Address 3385, Al Thomamah Road, An-Nada District.  
800 124 0201 | burujinsurance.com

**Issue Date:** 3 April 2025

# Vehicle Details

Submit the Vehicle Update Request

Owner Id Number7016158334

License issue date1445-12-27

Branch Id

Actual Driver Id Number

Plate registration typeEquipment

Sequence Number718279020

Vehicle Modelکرین

Vehicle Load1

Model Year2024

Chassis NumberLFCNNF5P7P3200514

MVPI StatusNot exist

Insurance StatusValid

Actual Driver Start Date

Ownership Start Date

license Expiry Date1448-12-27

Branch name

Actual Driver Name

Plate Info

|      |     |
|------|-----|
| ٣٧٨٤ | ١١١ |
| 3782 | AAA |

Vehicle Makerسانی

Vehicle Colorازرق

Vehicle Weight42500

Restriction StatusNot Restricted

Vehicle Statusvalid

MVPI Expiry Hijri Date

Insurance Expiry Date2025-11-14



## CERTIFICATE OF TEST AND THOROUGH EXAMINATION OF MOBILE CRANE

|                           |                                        |                              |
|---------------------------|----------------------------------------|------------------------------|
| <b>Cert. No.: 1876403</b> | <b>Date of Examination: 16/03/2025</b> | <b>Sticker No.: 01-74443</b> |
|---------------------------|----------------------------------------|------------------------------|

|                                               |                                |                                                                                                                |
|-----------------------------------------------|--------------------------------|----------------------------------------------------------------------------------------------------------------|
| Name & address of owner of the equipment      |                                | Sudhir Equipment Rental Company                                                                                |
| Inspection requested by                       |                                | Sudhir Equipment Rental Company                                                                                |
| Place of inspection                           |                                | DAMMAM                                                                                                         |
| Type of inspection                            |                                | TEST & THOROUGH EXAMINATION                                                                                    |
| Relevant regulation / Standard                |                                | ASME B30.5                                                                                                     |
| Date of previous inspection / load test       |                                |                                                                                                                |
| Identification & Description of the Equipment | Manufacturer name              | SANY                                                                                                           |
|                                               | Equipment Type                 | MOBILE CRANE                                                                                                   |
|                                               | Nature of power                | DEISEL POWERED                                                                                                 |
|                                               | Model / Year                   | SYM5433JQZ ( STC600T5 )/ 2024                                                                                  |
|                                               | Serial number                  | TC2060CE0540                                                                                                   |
|                                               | Owner ID / Registration number | SRC-STC-060-020                                                                                                |
|                                               | Rated Capacity (maximum)       | 60 TON                                                                                                         |
|                                               | Present Configuration          | Main hoist current capacity: 60 TON with 6 Part Of Line<br>Auxiliary hoist current capacity: 6 Ton with 1 Line |
|                                               | Radius (Mini / Max)            | Minimum: 3 m; Maximum: 36 m                                                                                    |
|                                               | Length of Boom                 | Minimum: 11.7 m; Maximum: 45.5 m                                                                               |
|                                               | Counterweight (mass)           | Standard from Manufacturer                                                                                     |
|                                               | Wire rope specification        | 18 mm                                                                                                          |
|                                               | Complementary devices          | -                                                                                                              |

|                                                                                                                                                                                                                                                                                    |                           |                   |                               |                  |                          |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------|-------------------|-------------------------------|------------------|--------------------------|
| <b>Description of test:</b><br>Visual & Function Test inspection was carried out, followed by full functional testing.<br>100 % Of SWL Load Test Was Carried Out<br><br><b>Note: "This certificate does not cover the use of the equipment for Personnel/Man riding purposes".</b> | <b>Length of boom (m)</b> | <b>Radius (m)</b> | <b>Reeving (No. of falls)</b> | <b>Test Load</b> | <b>Safe Working Load</b> |
|                                                                                                                                                                                                                                                                                    | 26.5 M                    | 20 M              | 6                             | 3.8 Ton          | 3.8 Ton                  |
|                                                                                                                                                                                                                                                                                    | -                         | -                 | -                             | -                | -                        |
|                                                                                                                                                                                                                                                                                    | -                         | -                 | -                             | -                | -                        |

### Result of Examination:

**The above mentioned equipment has been found satisfactory at the time of inspection and is considered to be safe for further use, subject to continuous maintenance being applied and qualified operator being employed.**

This is to certify that the Competent Person did attend at the said premises on said date to witness proof load test and/or to carry out thorough examination of the equipment described herein and that all particulars described above were correct at the time of examination. This Certificate becomes void in case of any major repair, modification and /or alteration being un-authorized by issuer of hereof.

|                                                                                 |                                                        |
|---------------------------------------------------------------------------------|--------------------------------------------------------|
| <b>Next Proof Load Test Due: 15/03/2030 or After Major Repair/Modifications</b> | <b>Next Inspection Due is on or before: 15/03/2026</b> |
|---------------------------------------------------------------------------------|--------------------------------------------------------|

Issued at Al Khobar on 17/03/2025

Inspector to Bureau Veritas  
Signature:

Name: Mohamed Elsabry  
Position: Inspector



Reviewed by  
Signature:

Name: Abdullah SHEHRI  
Position: Operations Manager

The technical conclusions thus expressed may have to be reconsidered in light of any modifications or alterations that would invalidate the data shown in the present certificate. These conclusions would become null & void should Bureau Veritas not be kept informed of such modifications or alterations with specific reference to the present certificate.  
Any person not a party to the contract pursuant to which this document is delivered may not assert a claim against Bureau Veritas for any liability arising out of errors or omissions which may be contained in said document, or for errors of judgement, fault or negligence committed by the personnel of the Society or of its Agents in the establishment or issuance of this document, and in connection with any activities for which it may provide.  
This not is NOT an indication that the item(s) is (are) fit for any specific purpose and does not release the manufacture, supplier and any party from their respective duty, guarantee, obligation and/or indemnity relating to, without limitation patents, workmanship, materials, safety, performance in operation and/or reliability.



## CHECKLIST OF TEST & THOROUGH EXAMINATION OF MOBILE CRANE

|                           |                                        |
|---------------------------|----------------------------------------|
| <b>Cert. No.: 1876403</b> | <b>Date of Examination: 16/03/2025</b> |
|---------------------------|----------------------------------------|

| SECTION                                 | CONDITION      | REMARKS |
|-----------------------------------------|----------------|---------|
| <b>1. ACCESS</b>                        |                |         |
| 1.1 Access to the cabin/control station | Satisfactory   |         |
| 1.2 Access for maintenance operation    | Satisfactory   |         |
| <b>2. CHASSIS</b>                       |                |         |
| 2.1 Chassis                             | Satisfactory   |         |
| 2.2 Traveling device (tire, crawler)    | Satisfactory   |         |
| 2.3 Outriggers                          | Satisfactory   |         |
| 2.4 Outrigger sole (shoe or pad)        | Satisfactory   |         |
| 2.5 None return valve on outrigger      | Satisfactory   |         |
| 2.6 Locking of suspensions              | Satisfactory   |         |
| 2.7 Locking of outriggers rest position | Satisfactory   |         |
| <b>3. STRUCTURE OF EQUIPMENT</b>        |                |         |
| 3.1 Structure, A frame                  | Satisfactory   |         |
| 3.2 Jib, fly jib                        | Satisfactory   |         |
| 3.3 Pendants                            | Satisfactory   |         |
| 3.4 Counter weight                      | Satisfactory   |         |
| <b>4. MECHANISM</b>                     |                |         |
| 4.1 Main Hoisting mechanism             | Satisfactory   |         |
| 4.2 Aux. Hoisting mechanism             | Satisfactory   |         |
| 4.3 Hydraulic system                    | Satisfactory   |         |
| 4.4 Cylinders                           | Satisfactory   |         |
| 4.5 Hoisting brake system               | Satisfactory   |         |
| 4.6 Limitation of the lowering speed    | Satisfactory   |         |
| 4.7 Telescoping mechanism               | Satisfactory   |         |
| 4.8 Luffing mechanism                   | Not applicable |         |
| 4.9 Pivoting joints                     | Satisfactory   |         |
| 4.10 Brake of slewing motion            | Satisfactory   |         |



|                                        |              |  |
|----------------------------------------|--------------|--|
| 4.11 Traveling Brake                   | Satisfactory |  |
| 4.12 Guards for moving parts           | Satisfactory |  |
| 4.13 Motor                             | Satisfactory |  |
| 4.14 Gear box                          | Satisfactory |  |
| <b>5. LIFTING SYSTEM</b>               |              |  |
| 5.1 Wire rope / chain                  | Satisfactory |  |
| 5.2 Wire/chain rope end termination    | Satisfactory |  |
| 5.3 Drum, pulley, return pulley        | Satisfactory |  |
| 5.4 Hooks & hook blocks                | Satisfactory |  |
| 5.5 Other load handling devices        | Satisfactory |  |
| <b>6. ENERGY</b>                       |              |  |
| 6.1 Main switch locking                | Satisfactory |  |
| 6.2 Equipment and cabling              | Satisfactory |  |
| 6.3 Protection of live parts/enclosure | Satisfactory |  |
| 6.4 Lighting of the crane/site         | Satisfactory |  |
| <b>7. CABIN / CONTROL STATION</b>      |              |  |
| 7.1 Structure                          | Satisfactory |  |
| 7.2 Visibility / windows               | Satisfactory |  |
| 7.3 Heating / AC system                | Satisfactory |  |
| 7.4 Seat                               | Satisfactory |  |
| 7.5 Fire extinguisher                  | Satisfactory |  |
| 7.6 Identification of the controls     | Satisfactory |  |
| 7.7 Control dead man type              | Satisfactory |  |
| 7.8 General stopping device by key     | Satisfactory |  |
| 7.9 Emergency stop button              | Satisfactory |  |
| 7.10 Level indicator                   | Satisfactory |  |
| 7.11 Angle Indicator                   | Satisfactory |  |
| 7.12 Horn                              | Satisfactory |  |
| 7.13 Traffic lights                    | Satisfactory |  |
| 7.14 Direction Indicators              | Satisfactory |  |
| <b>8. SAFETY DEVICES</b>               |              |  |



BUREAU  
VERITAS



|                                           |                |  |
|-------------------------------------------|----------------|--|
| 8.1 Hoisting limiter/Anti Two Blocks      | Satisfactory   |  |
| 8.2 Luffing limiter                       | Not applicable |  |
| 8.3 Telescopic limiter                    | Satisfactory   |  |
| 8.4 Slewing limiter                       | Satisfactory   |  |
| 8.5 Load limiter                          | Satisfactory   |  |
| 8.6 Level limiter                         | Satisfactory   |  |
| 8.7 Rated capacity indicator (RCI) / ASLI | Satisfactory   |  |
| 8.8 None return valve on piston           | Satisfactory   |  |
| 8.9 Other limiter or indicator            | Satisfactory   |  |

#### 9. MISCELLANEOUS REQUIREMENTS

|                                 |              |  |
|---------------------------------|--------------|--|
| 9.1 Maker plate                 | Satisfactory |  |
| 9.2 Load chart                  | Satisfactory |  |
| 9.3 Wire rope certificate       | Satisfactory |  |
| 9.4 General Safety Requirements | Satisfactory |  |

Notes : Plate No : 1957 / ZAA

Main Hook No : BI00085(127404237) SWL : 80 Ton

AUX Hook NO : BH00091 ( 127400272 ) SWL : 7 Ton

Next Proof Load Test Due: 15/03/2030 or After Major Repair/Modifications

Next Inspection Due is on or before: 15/03/2026

Inspector to Bureau Veritas

Signature:

*Mohamed Elsabry*



Name: Mohamed Elsabry

Position: Inspector





## Bureau Veritas, Saudi Arabia

8th Floor, Danah Business Tower, Olaya District, Al Khobar, Kingdom of Saudi Arabia

Tel No : +966 13 882 1071

Web : <https://middle-east.bureauveritas.com>



Report No.: 246827

|                                                        |                                     |                                |                      |                                         |                                       |             |
|--------------------------------------------------------|-------------------------------------|--------------------------------|----------------------|-----------------------------------------|---------------------------------------|-------------|
| LIFTING EQUIPMENT<br>INSPECTION REPORT                 | Area<br>DAMMAM                      | Inspection Date<br>08/10/2025  |                      | Inspection Time<br>15:00                | Previous Sticker                      |             |
|                                                        |                                     |                                |                      |                                         | No.24-4148                            | Issue By BV |
| Department / Contractor<br>SUDHIR EQUIPMENT RENTAL CO. | Equipment Number<br>SRC-STC-060-020 | Equipment Location<br>DMM YARD |                      | Inspection Result<br>Pass               | New Sticker No.<br>BV-1383            |             |
| Manufacturer<br>SANY                                   | Model<br>STC600T5                   | Capacity<br>60 TON             | Type<br>Mobile Crane | Equipment Serial Number<br>TC2060CE0540 | Sticker Expiration Date<br>07/01/2026 |             |

Above Equipment was inspected by Bureau Veritas in accordance with applicable Saudi Aramco GI's, ASME and API Standards. Deficiencies that require corrective action are listed below. Specific repairs to correct each deficiency should be noted in the corrective action taken column.

| No.                            | DEFICIENCIES / NOTES                                                                                                                                                                                                                                                                                                                                                                                                                                                  | Corrective Action Taken                  |
|--------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------|
| 1                              | <ul style="list-style-type: none"><li>-PERIODIC INSPECTION AND FUNCTION TEST FOR TRUCK MOUNTED MOBILE CRANE AS PER AS S.ARAMCO GI 7.030 AND ASME B30.5</li><li>-MAIN HOOK BLOCK S/N:HCZ2455022 , SWL: 60 TON @ 6 FALLS</li><li>- AUX HOOK S/N: YM20240031905, SWL: 6 TON @ 1FALL</li><li>- FLY JIB WAS STOWED</li><li>-REGISTRATION PLATE #3782 AAA</li><li>-EQUIPMENT WAS FOUND SATISFACTORY AT THE TIME OF INSPECTION</li><li>-FOLLOW PROPER PM REGULARLY</li></ul> |                                          |
| <b>Receiver Name :</b><br>ARIF |                                                                                                                                                                                                                                                                                                                                                                                                                                                                       | <b>Inspector Name :</b><br>MOHAMED OMARA |
| <b>Badge No.:</b><br>-         | <b>Telephone No.:</b><br>-                                                                                                                                                                                                                                                                                                                                                                                                                                            | <b>Telephone :</b><br>055 078 7628       |

When re-inspection is requested, a complete copy of this report should be ready review by the inspector.

|                                          |                                              |                                  |                                                  |                                                           |                                                  |
|------------------------------------------|----------------------------------------------|----------------------------------|--------------------------------------------------|-----------------------------------------------------------|--------------------------------------------------|
| <b>SAUDI ARAMCO INSPECTION CHECKLIST</b> |                                              |                                  | SAIC NUMBER<br><b>SAIC-U-7007</b>                | ISSUE DATE<br><b>12-Jan-23</b>                            | DISCIPLINE<br><b>ELEVATING/LIFTING EQUIPMENT</b> |
| <b>MOBILE / CRAWLER CRANES</b>           |                                              |                                  |                                                  |                                                           |                                                  |
| PROJECT TITLE                            |                                              |                                  | WBS/BI/JO NUMBER                                 | INSPECTION COMPANY<br><b>Bureau Veritas, Saudi Arabia</b> |                                                  |
| EQUIPMENT ID NUMBER :<br>SRC-STC-060-020 | EQUIPMENT DESCRIPTION/TYPE :<br>Mobile Crane |                                  | SERIAL NO. :<br>TC2060CE0540                     | REPORT No.: 246827                                        |                                                  |
| CAPACITY (SWL) :<br>60 TON               | MANUFACTURER :<br>SANY                       |                                  | FACILITY / LOCATION :<br>DMM YARD                |                                                           |                                                  |
| REQUESTED INSPECTION DATE :              | RFI No.                                      | TASK COMPLETED DATE : 08/10/2025 | EQUIPMENT OWNER :<br>SUDHIR EQUIPMENT RENTAL CO. |                                                           |                                                  |

## ACCEPTANCE CRITERIA

### 1.0 GENERAL REQUIREMENTS

|     |                                                                                                                                                                  | REFERENCE                   | PASS | FAIL | NA | REMARKS |
|-----|------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------|------|------|----|---------|
| 1.1 | Equipment documentation is available                                                                                                                             | ASME B30.5                  | ✓    |      |    |         |
| 1.2 | Preventive Maintenance is established and updated records are maintained                                                                                         | ASME B30.5 Sec:5-2.3.1      | ✓    |      |    |         |
| 1.3 | Daily pre-operational inspection checklists are checked                                                                                                          | GI 7.030 Para: 5.1.2        | ✓    |      |    |         |
| 1.4 | Vehicle government registration card (ISTIMARA) and Government periodic inspection are maintained and valid at all times for equipment that has a vehicle plate. | GI 7.030 Para: 7.1.2 Note:5 | ✓    |      |    |         |
| 1.5 | Durable load chart is provided in an accessible location                                                                                                         | ASME B30.5                  | ✓    |      |    |         |
| 1.6 | Work areas chart is available                                                                                                                                    | ASME B30.5                  | ✓    |      |    |         |
| 1.7 | Operator is certified (for the inspected crane type/model) and licensed                                                                                          | G.I. 7.025                  | ✓    |      |    |         |
| 1.8 | A sign is posted warning the operator not to rely solely on any automatic device as a substitute for safe operating practice                                     | G.I. 7.030                  | ✓    |      |    |         |
| 1.9 | Crane is painted safety yellow                                                                                                                                   | SAES-B067                   |      |      | ✓  |         |

|      |                                                                                                              | REFERENCE  | PASS | FAIL | NA | REMARKS |
|------|--------------------------------------------------------------------------------------------------------------|------------|------|------|----|---------|
| 1.10 | Crane is painted safety yellow-and-black stripes on offshore facilities                                      | SAES-B067  |      |      | ✓  |         |
| 1.11 | Rated capacity of crane is marked (Arabic & English)                                                         | SAES-B067  | ✓    |      |    |         |
| 1.12 | Fire extinguisher is in place with minimum rating 10 BC                                                      | ASME B30.5 | ✓    |      |    |         |
| 1.13 | Markings and direction of all control levers are clearly displayed                                           | ASME B30.5 | ✓    |      |    |         |
| 1.14 | Crane backward stability is in accordance with manufacturers standard (minimum radius and no load condition) | ASME B30.5 | ✓    |      |    |         |

## 2.0 INSPECTION POINTS (MOBILE & CRAWLER CRANES)

|     |                                                                                        | REFERENCE  | PASS | FAIL | NA | REMARKS |
|-----|----------------------------------------------------------------------------------------|------------|------|------|----|---------|
| 2.1 | Load- holding check valve for boom is operational                                      | ASME B30.5 | ✓    |      |    |         |
| 2.2 | Two (2) full wraps of rope remain on the drum when hook is in the extreme low position | ASME B30.5 | ✓    |      |    |         |
| 2.3 | Swing control is smoothly operating on acceleration and deceleration                   | ASME B30.5 | ✓    |      |    |         |
| 2.4 | Swing braking operates, as well as positive locking devices (manual and auto)          | ASME B30.5 | ✓    |      |    |         |
| 2.5 | Travel controls are properly operating/functioning                                     | ASME B30.5 | ✓    |      |    |         |
| 2.6 | Auxiliary travel controls function correctly for multiple control- station cranes      | ASME B30.5 | ✓    |      |    |         |
| 2.7 | Travel brakes and locks for crawler cranes are correctly operating                     | ASME B30.5 |      |      | ✓  |         |
| 2.8 | Travel brakes and locks for wheel-mounted cranes are correctly operating               | ASME B30.5 | ✓    |      |    |         |

|      |                                                                                     | REFERENCE  | PASS | FAIL | NA | REMARKS |
|------|-------------------------------------------------------------------------------------|------------|------|------|----|---------|
| 2.9  | Power plant controls of superstructure -mounted power plant working properly        | ASME B30.5 | ✓    |      |    |         |
| 2.10 | Rotation-resistant and fiber-core ropes are not used for boom hoist reeving         | ASME B30.5 |      |      | ✓  |         |
| 2.11 | Sheave grooves have surface smoothness without any defects                          | ASME B30.5 | ✓    |      |    |         |
| 2.12 | Sheave guards are in place on the lower block                                       | ASME B30.5 | ✓    |      |    |         |
| 2.13 | All sheaves can be lubricated (except permanently lubricated types)                 | ASME B30.5 | ✓    |      |    |         |
| 2.14 | All cab glazing's are safety glazing material                                       | ASME B30.5 | ✓    |      |    |         |
| 2.15 | Verify cab doors functionality and condition                                        | ASME B30.5 | ✓    |      |    |         |
| 2.16 | Seat belt is fitted and in good condition                                           | ASME B30.5 | ✓    |      |    |         |
| 2.17 | Walking platforms and areas of structure are skid-resistance                        | ASME B30.5 | ✓    |      |    |         |
| 2.18 | Guard rails are fitted for crawler cranes                                           | ASME B30.5 |      |      | ✓  |         |
| 2.19 | Fixed or telescoping bumper for boom stop is functional (if fitted)                 | ASME B30.5 |      |      | ✓  |         |
| 2.20 | Shock absorbing bumper for boom stop is functional (if fitted)                      | ASME B30.5 |      |      | ✓  |         |
| 2.21 | Hydraulic boom elevating cylinder, used as boom stop, is functional (if fitted)     | ASME B30.5 | ✓    |      |    |         |
| 2.22 | Boom angle indicator is fitted, operable, and can be read from the operator station | ASME B30.5 | ✓    |      |    |         |
| 2.23 | Boom shut-off or hydraulic relief is provided for high angle boom condition         | ASME B30.5 | ✓    |      |    |         |
| 2.24 | Boom length indicator is fitted for telescoping booms and is working                | ASME B30.5 | ✓    |      |    |         |

|      |                                                                                                                     | REFERENCE                  | PASS | FAIL | NA | REMARKS |
|------|---------------------------------------------------------------------------------------------------------------------|----------------------------|------|------|----|---------|
| 2.25 | Anti-two-blocking devices are fitted and working (main and auxiliary)                                               | ASME B30.5                 | ✓    |      |    |         |
| 2.26 | Operation and accuracy of the fitted LMI (compare with load chart over a range of angles and radii)                 | ASME B30.5                 | ✓    |      |    |         |
| 2.27 | LMI is fitted, operational and accurate for bool length, rated load, angle, radius, etc. (for 3 ton cranes or more) | ASME B30.5 Sec: 5-1.9.10.2 | ✓    |      |    |         |
| 2.28 | Outriggers and jacks are not leaking oil                                                                            | ASME B30.5                 | ✓    |      |    |         |
| 2.29 | Jack is in good operating condition at each outrigger                                                               | ASME B30.5                 | ✓    |      |    |         |
| 2.30 | Each outrigger jack locking device is functional (if fitted)                                                        | ASME B30.5                 | ✓    |      |    |         |
| 2.31 | No leakage from each jack seal when the crane is jacked up                                                          | ASME B30.5                 | ✓    |      |    |         |
| 2.32 | Outrigger jack bolts are fully secure                                                                               | ASME B30.5                 | ✓    |      |    |         |
| 2.33 | All road wheel nuts are fully secure                                                                                | ASME B30.5                 | ✓    |      |    |         |
| 2.34 | All tyres are serviceable and without damage or excess wear                                                         | ASME B30.5                 | ✓    |      |    |         |
| 2.35 | Fuel tank supports and straps are secure                                                                            | ASME B30.5                 | ✓    |      |    |         |
| 2.36 | Hydraulic oil tank supports and straps are secure                                                                   | ASME B30.5                 | ✓    |      |    |         |
| 2.37 | Underside of chassis shows no obvious faults                                                                        | ASME B30.5                 | ✓    |      |    |         |
| 2.38 | Outrigger boxes are not cracked                                                                                     | ASME B30.5                 | ✓    |      |    |         |
| 2.39 | Front and rear steering cylinder anchor points and pins are secure                                                  | ASME B30.5                 | ✓    |      |    |         |
| 2.40 | Track rod end joints are not worn and are secure                                                                    | ASME B30.5                 | ✓    |      |    |         |
| 2.41 | Axle bolts and nuts are fully secure                                                                                | ASME B30.5                 | ✓    |      |    |         |
| 2.42 | Wheel hub oil seals are not leaking                                                                                 | ASME B30.5                 | ✓    |      |    |         |

|          |                                                                                                                                                                                                                                                         | REFERENCE  | PASS | FAIL | NA | REMARKS |
|----------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------|------|------|----|---------|
| 2.43     | Brake linings are not oil contaminated                                                                                                                                                                                                                  | ASME B30.5 | ✓    |      |    |         |
| 2.44     | Brake hoses have not deteriorated, e.g. cracks, splits, leaks, etc.                                                                                                                                                                                     | ASME B30.5 | ✓    |      |    |         |
| 2.45     | All chassis cross members are not cracked or corroded                                                                                                                                                                                                   | ASME B30.5 | ✓    |      |    |         |
| 2.46     | Transmission mounting bolts and bushings are secure                                                                                                                                                                                                     | ASME B30.5 | ✓    |      |    |         |
| 2.47     | All drive shaft bolts and universal joints are not worn                                                                                                                                                                                                 | ASME B30.5 | ✓    |      |    |         |
| 2.48     | Ring gear bolts are fully secure                                                                                                                                                                                                                        | ASME B30.5 | ✓    |      |    |         |
| 2.49     | All hydraulic hoses under chassis have not deteriorated (cracks , splits , leaks)                                                                                                                                                                       | ASME B30.5 | ✓    |      |    |         |
| 2.50     | Engine shows no major oil leakage                                                                                                                                                                                                                       | ASME B30.5 | ✓    |      |    |         |
| 2.51     | Radiator does not leak water                                                                                                                                                                                                                            | ASME B30.5 | ✓    |      |    |         |
| 2.52 (a) | Rope is free of damages: 1 broken wire protruding from the core Wear of 1/3 of the original diameter of outside individual wires Kinking, crushing, birdcaging or other distortion                                                                      | ASME B30.5 | ✓    |      |    |         |
| 2.52 (b) | For running ropes: Max of 6 randomly broken wires in 1 lay or 3 broken wires in 1 strand of 1 lay, For rotation resistance ropes: 2 randomly distributed broken wires in six rope diameters or 4 randomly distributed broken wires in 30 rope diameters | ASME B30.5 | ✓    |      |    |         |
| 2.52(c)  | Evidence of any heat damage from any cause Reduction below nominal diameter                                                                                                                                                                             | ASME B30.5 | ✓    |      |    |         |
| 2.53     | Main hoist drum mounting bolts are secure                                                                                                                                                                                                               | ASME B30.5 | ✓    |      |    |         |
| 2.54     | Rear telescope side and top wear pads are serviceable                                                                                                                                                                                                   | ASME B30.5 | ✓    |      |    |         |
| 2.55     | Bottom and side wear pads of telescope sections are serviceable                                                                                                                                                                                         | ASME B30.5 | ✓    |      |    |         |
| 2.56     | Center swivel coupling pipes and hoses do not leak                                                                                                                                                                                                      | ASME B30.5 | ✓    |      |    |         |

|      |                                                                                                                         | REFERENCE  | PASS | FAIL | NA | REMARKS |
|------|-------------------------------------------------------------------------------------------------------------------------|------------|------|------|----|---------|
| 2.57 | Center swivel coupling bolts are all secure                                                                             | ASME B30.5 | ✓    |      |    |         |
| 2.58 | Boom lift cylinder anchor bolts and bushings are secure                                                                 | ASME B30.5 | ✓    |      |    |         |
| 2.59 | Swing gearbox mounting bolts are secure                                                                                 | ASME B30.5 | ✓    |      |    |         |
| 2.60 | Swing gearbox bottom oil seal and drive gear are in a serviceable condition (Should be well lubricated)                 | ASME B30.5 | ✓    |      |    |         |
| 2.61 | Wire rope clips shall be drop-forged steel of the single saddle U bolt or doubled saddle type clip for end termination. | ASME B30.5 | ✓    |      |    |         |
| 2.62 | Emergency switch / Power take off switch need to be verified                                                            | ASME B30.5 | ✓    |      |    |         |

### 3.0 CRANE CAB

|      |                                                                                    | REFERENCE   | PASS | FAIL | NA | REMARKS |
|------|------------------------------------------------------------------------------------|-------------|------|------|----|---------|
| 3.1  | Horn and wind speed anemometer are working                                         | ASME B30.5  | ✓    |      |    |         |
| 3.2  | Crane level indicator is fitted and working                                        | ASME B30.5  | ✓    |      |    |         |
| 3.3  | Engine gauges and associated indicators are working                                | ASME B30.5  | ✓    |      |    |         |
| 3.4  | The warning sign stating power line required clearances is visible to the operator | ASME B30.5  | ✓    |      |    |         |
| 3.5  | Load block sheaves turn freely and are undamaged                                   | ASME B30.5  | ✓    |      |    |         |
| 3.7  | Hook assemblies are equipped with safety latches                                   | ASME B30.5  | ✓    |      |    |         |
| 3.8  | Hook assembly labeling and manufacturer data is clearly marked                     | ASME B30.10 | ✓    |      |    |         |
| 3.9  | Hook's weight is clearly marked/printed on the hook                                | ASME B30.10 | ✓    |      |    |         |
| 3.10 | Safe working load of hook is clearly marked on the item                            | ASME B30.10 | ✓    |      |    |         |

|      |                                                                                                                                                 | REFERENCE                          | PASS | FAIL | NA | REMARKS |
|------|-------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------|------|------|----|---------|
| 3.11 | Hook does not show defects such as nicks, cracks and gouges                                                                                     | ASME B30.10                        | ✓    |      |    |         |
| 3.12 | Hook is not bent or twisted                                                                                                                     | ASME B30.10                        | ✓    |      |    |         |
| 3.13 | Hook is not distorted in the throat opening - Max. allowable throat opening is 15% compared to new hook, or as per manufacturer recommendations | ASME B30.10                        | ✓    |      |    |         |
| 3.14 | Maximum wear in the hook bowl is not exceeding 10% (compared to new hook) or as per manufacturer recommendations                                | ASME B30.10                        | ✓    |      |    |         |
| 3.15 | Hook is not cracked, gouged or shows nicks                                                                                                      | ASME B30.10                        | ✓    |      |    |         |
| 3.16 | Hook can lock (if it is a self-locking hook)                                                                                                    | ASME B30.10                        |      |      | ✓  |         |
| 3.17 | Inoperative latch (if provided) — any damaged latch or malfunctioning latch that does not close the hook's throat                               | ASME B30.10 Sec :<br>10-1.10.5 (i) | ✓    |      |    |         |
| 3.18 | Rope guards and locked in position with pins (hook block)                                                                                       | ASME B30.5                         | ✓    |      |    |         |
| 3.19 | Dead end rope anchor is fitted with a lock pin (hook block)                                                                                     | ASME B30.5                         | ✓    |      |    |         |
| 3.20 | Dead end rope anchor is correctly made with a suitable wedge socket and loop- back termination                                                  | ASME B30.5                         | ✓    |      |    |         |
| 3.21 | Reverse travel alarm is operational                                                                                                             | ASME B30.5                         | ✓    |      |    |         |
| 3.22 | Turning signals and indicators are working correctly                                                                                            | ASME B30.5                         | ✓    |      |    |         |
| 3.23 | Road lighting, including spotlights, are in good condition and operable                                                                         | ASME B30.5                         | ✓    |      |    |         |
| 3.24 | Dry friction brakes and clutches shall be protected against rain and other liquids such as oil and lubricants                                   | ASME B30.5 Sec 5-1.9.8             | ✓    |      |    |         |



## 4.0 CRAWLER CRANE

|      |                                                                                                   | REFERENCE                      | PASS | FAIL | NA | REMARKS |
|------|---------------------------------------------------------------------------------------------------|--------------------------------|------|------|----|---------|
| 4.1  | Track pads are undamaged                                                                          | ASME B30.5                     |      |      | ✓  |         |
| 4.2  | Drive sockets and tumblers are serviceable                                                        | ASME B30.5                     |      |      | ✓  |         |
| 4.3  | Top and bottom swing rollers and tracks are in good overall condition (Should be well lubricated) | ASME B30.5                     |      |      | ✓  |         |
| 4.4  | Track idlers are serviceable                                                                      | ASME B30.5                     |      |      | ✓  |         |
| 4.5  | Back boom stops are functioning                                                                   | ASME B30.5                     |      |      | ✓  |         |
| 4.6  | Back A-Frame is in good condition                                                                 | ASME B30.5                     |      |      | ✓  |         |
| 4.7  | Boom cut-out (at maximum angle) is operable                                                       | ASME B30.5                     |      |      | ✓  |         |
| 4.8  | Power low lowering is operational                                                                 | ASME B30.5                     |      |      | ✓  |         |
| 4.9  | Boom hoist safety auxiliary ratchet / pawl lock is engaging                                       | ASME B30.5 Sec:<br>5-1.3.1(c)  |      |      | ✓  |         |
| 4.10 | Boom chords and lacings are undamaged (bent)                                                      | ASME B30.5                     |      |      | ✓  |         |
| 4.11 | Sheave grooves are free from surface defects that could cause rope damage.                        | ASME B30.5 Sec: 5-1.7.4<br>(a) |      |      | ✓  |         |
| 4.12 | Pendant ropes are showing no broken wires (see 2.0.55)                                            | ASME B30.5                     |      |      | ✓  |         |
| 4.13 | Operation of steering brakes is satisfactory                                                      | ASME B30.5                     |      |      | ✓  |         |
| 4.14 | Main machinery guarding is in place                                                               | ASME B30.5                     |      |      | ✓  |         |
| 4.15 | Main clutch is fully operational                                                                  | ASME B30.5                     |      |      | ✓  |         |
| 4.16 | Main boom and hoist drum brakes are fully functional                                              | ASME B30.5                     |      |      | ✓  |         |

## REMARKS

### REFERENCE DOCUMENTS:

- 1- ASME B30.5 - 2021 Issue: Mobile & Locomotive Cranes
- 2- ASME B30.10 - 2019 Issue: Hooks
- 3- SAES-B067 - 2020 Issue: Safety Identification and Safety Colors
- 4- SA GI 7.025-2018 Issue: Heavy Equipment Operator and Rigger Testing and Certification
- 5- SA GI 7.030 - 2023 Issue: Inspection and Testing Requirements for Elevating/Lifting Equipment

## Signature

Inspected / Witnessed by 3rd Party Certified Inspector

**Name** MOHAMED OMARA

**Signature**



**Certificate No.** 80019106

**Company** Bureau Veritas

## User Representative

**Name** ARIF

**Signature**



**Date** 08/10/2025



**Sticker No:**  
**BV-1383**

**Bureau Veritas**  
Tel.: + 966 013 822  
1071  
Fax: + 966 013 822  
1072  
Al Khobar, Saudi  
Arabia



**EQUIP .S.N: TC2060CE0540**

**EQUIP .NO : SRC-STC-060-020**

**EQUIP.SWL : 60 TON**


**INSPECTION DATE : 08/10/2025**

**NEXT INSPECTION DATE :07/01/2026**

**INSPECTOR NAME: MOHAMED OMARA**

**SAP # 80019106**

**SA INSPECTION DEPARTMENT APPROVED CONTRACTOR AGENCY**



## MAGNETIC PARTICLE TESTING REPORT

Customer Name :- SUDHIR EQUIPMENT RENTAL Date of Inspection:- 9, October, 2025  
Job No. :- 25-1154 Next Inspection Date :- 8 April, 2026  
Work Location. :- Inspection Report No.:- NDT-I-25-1154-01

Material Description :- HOOK BLOCK Serial # :- HCZ2455022(OZG60.18A) QTY 1

Area Inspected: Critical areas

### Inspection Method

Magnetizing Process : ☒ Continuous ☐ Residual

Magnetization : ☐ Alternating (AC) ☐ Direct (DC) Magnetic Particles: ☐ Dry ☐ Wet ☒ Visible ☐ Fluorescent

### Traceability & Certification Calibration #

☐ AC Yoke ☐ DC Coil ☒ Permanent Magnet ☐ UV Light ☐ Other

No. No. No. 5321 No. No.

Calib. Cert. 16-NOV-2024

Due Date 16-NOV-2025

Batch No.

Black Magnetic Ink:

MAGNAFLUX 211101

White Contrast:

MAGNAFLUX 231003

Surface Condition : Cleaned to Base Metal

Background : ☒ White ☐ Ground ☐ Non-treated

Specification : ☐ API ☐ DS1 ☒ ASTM ☐ ASME ☐ AWS ☒ Other ASTM E709

Acceptance Criteria : ☐ DS1 ☒ ASTM ☐ ASME ☒ AWS Edition AWS D1.1 & ASTM E709

### Result

Magnetic particle inspection was carried out on above description critical & available area and found free from surface cracks or flaws at the time of inspection

(ACCEPTED)



\* Certificate is not valid unless QC signature and stamp are on report


Inspector Name: Ibrahim Abdullah

NDT LEVEL TWO



Hany Akif

Reviewed By



## MAGNETIC PARTICLE TESTING REPORT

Customer Name :- SUDHIR EQUIPMENT RENTAL Date of Inspection:- 9, October, 2025  
Job No. :- 25-1154 Next Inspection Date :- 8 April, 2026  
Work Location. :- Inspection Report No.:- NDT-I-25-1154-02

Material Description :- AUXILIARY HOOK Serial # :- M2024031905 QTY 1

Area Inspected: Critical areas

### Inspection Method

Magnetizing Process : ☒ Continuous ☐ Residual

Magnetization : ☐ Alternating (AC) ☐ Direct (DC) Magnetic Particles: ☐ Dry ☐ Wet ☒ Visible ☐ Fluorescent

### Traceability & Certification Calibration #

☐ AC Yoke ☐ DC Coil ☒ Permanent Magnet ☐ UV Light ☐ Other

No. No. No. 5321 No. No.

Calib. Cert. 16-NOV-2024

Due Date 16-NOV-2025

Batch No.

Black Magnetic Ink:

MAGNAFLUX 211101

White Contrast:

MAGNAFLUX 231003

Surface Condition : Cleaned to Base Metal

Background : ☒ White ☐ Ground ☐ Non-treated



Specification : ☐ API ☐ DS1 ☒ ASTM ☐ ASME ☐ AWS ☒ Other ASTM E709

Acceptance Criteria : ☐ DS1 ☒ ASTM ☐ ASME ☒ AWS Edition AWS D1.1 & ASTM E709

### Result

Magnetic particle inspection was carried out on above description critical & available area and found free from surface cracks or flaws at the time of inspection

(ACCEPTED)

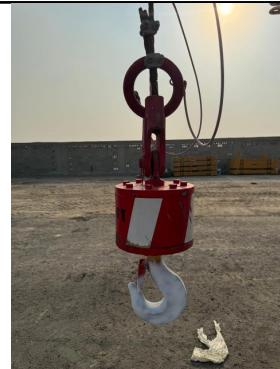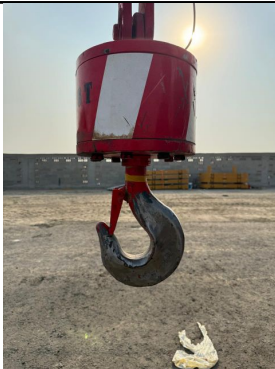

\* Certificate is not valid unless QC signature and stamp are on report

Inspector Name: Ibrahim Abdullah

NDT LEVEL TWO



Hany Akif

Reviewed By
