OWNERSHIP CERTIFICATE

To Whom It May Concern

This is to certify that the following equipment listed below is the sole property of Sudhir Equipment Rental Company:

Equipment	**AWP**
Brand / Make	**DINGLI**
Asset ID	**S16SD-2679**
Model Number	**BT16CRT2**
Serial Number	**BTRC025G00148**
Working Height	**16 Meter**
Type	**Diesel Telescopic Boom**
Manufacturing Year	**2025**

This certification is issued to confirm the ownership status of the aforementioned equipment. Sudhir Equipment Rental Company holds full legal ownership rights over the listed equipment and retains all associated benefits and responsibilities.

Should there be any queries or requests for verification regarding the ownership of the mentioned equipment, please do not hesitate to contact us at: Info@sudhirrentals.com

Sincerely,

شركة سودهير لتأجير المعدات
الدمام
س.ت ٢٠٥٠١٣٠٠٥٣
C.R. 2050130053
Dammam
SUDHIR EQUIPMENT RENTAL COMPANY

Rajesh Thakur
Plant Manager
Sudhir Equipment Rental Company

Certificate of Insurance

Policy Holder Name	Sudhir Equipment Rental Company	**اسم حامل الوثيقة**
Policy Number	5/EP/30425/0/0	**رقم الوثيقة**
Original Policy Period	05/04/2026 to 04/04/2027	**فترة الوثيقة الأصلية**

Gulf Insurance Group certifies that above client is holding Contractor's Plant & Machinery Insurance Policy for the below mentioned Equipment in accordance with the above mentioned Insurance Policy:

تشهد مجموعة الخليج للتأمين بأن العميل المذكور أعلاه يحمل وثيقة تأمين على معدات والات المقاولين للمعدة المذكورة أدناه, و ذلك وفقا لشروط وثيقة التأمين المذكورة أعلاه:

Asset ID	:	S16SD-2679	:	**معرف الأصل**
Brand	:	DINGLI	:	**العلامة التجارية**
Type	:	BT16CRT2	:	**النوع**
Model	:	AWPS	:	**الطراز**
Manufacturing Year	:	2025	:	**سنة الصنع**
Equipment Serial Number	:	BTRC025G00148	:	**الرقم التسلسلي للمعدة**
Insurance Effective Date	:	05/04/2026	:	**تاريخ سريان التأمين**

This Certificate has been issued upon Insureds request as per all terms and conditions, exclusions, warranties mentioned in the policy.

تم اصدار هذة الشهادة بناء على طلب المؤمن له وذلك حسب الشروط والاستثناءات والاشتراطات المذكورة في الوثيقة

Al Khobar : 01st April 2026

Signature of Insurer's Authorized Representative

PUBLIC

CERTIFICATE OF TEST AND THOROUGH EXAMINATION OF ELEVATION WORK PLATFORM

Cert. No.: 2287493	Date of Examination: 09/08/2026	Sticker No.: 01-100991

Name & address of owner of the equipment		Sudhir Equipment Rental Company
Inspection requested by		Sudhir Equipment Rental Company
Place of inspection		Dammam Yard
Type of inspection		Visual Inspection And Function Test
Relevant regulation / Standard		ANSI 92.5
Date of previous inspection / load test		
Identification & Description of the Equipment	Manufacturer name	Dingli
	Equipment Type	Boom Supported Elevation Work Platform (Man Lift)
	Model / Year	BT16CRT2
	Serial number	BARC025G00148
	Owner ID / Registration number	S16SD-2679
	Nature of power	Diesel
	Rated Capacity (SWL)	320 KG (2 Persons STD)
	Max. Platform height:	16.27 MTR
	Max. Horizontal reach:	-

Description of test:
- Visual Inspection And Function Test Was Carried Out
- And Found No Defects And Satisfactory At The Time Of Inspection

TEST LOAD	S.W.L.
-	320 KG (2 Persons STD)

Result of Examination:
The above mentioned equipment has been found satisfactory at the time of inspection and is considered to be safe for further use, subject to continuous maintenance being applied and qualified operator being employed.

This is to certify that the Competent Person did attend at the said premises on said date to witness proof load test and/or to carry out thorough examination of the equipment described herein and that all particulars described above were correct at the time of examination. This Certificate becomes void in case of any major repair, modification and /or alteration being un-authorized by issuer of hereof.

Next Proof Load Test Due: After Major Repair/Modifications	Next Inspection Due is on or before: 08/02/2027

Issued at Al Khobar on 09/08/2026

Inspector to Bureau Veritas
Signature:



Name: Mohamed Elsabry
Position: Inspector



Reviewed by
Signature:



Name: Ahmed Elabady
Position: Reviewer

The technical conclusions thus expressed may have to be reconsidered in light of any modifications or alterations that would invalidate the data shown in the present certificate. These conclusions would become null & void should Bureau Veritas not be kept informed of such modifications or alterations with specific reference to the present certificate.
Any person not a party to the contract pursuant to which this document is delivered may not assert a claim against Bureau Veritas for any liability arising out of errors or omissions which may be contained in said document, or for errors of judgement, fault or negligence committed by the personnel of the Society or of its Agents in the establishment or issuance of this document, and in connection with any activities for which it may provide.
This not is NOT an indication that the item(s) is (are) fir for any specific purpose and does not release the manufacture, supplier and any party from their respective duty, guarantee, obligation and/or indemnity relating to, without limitation patents, workmanship, materials, safety, performance in operation and/or reliability.

CHECKLIST OF TEST AND THOROUGH EXAMINATION OF ELEVATION WORK PLATFORM

SECTION	CONDITION/REMARKS
1. ACCESS	
1.1 Access to the cabin/control station	Satisfactory
1.2 Access for maintenance operation	Satisfactory
2. STRUCTURE OF EQUIPMENT	
2.1 Boom sections	Satisfactory
2.2 Bolts & rivets	Satisfactory
2.3 Connecting pins	Satisfactory
2.4 Chassis structure	Satisfactory
2.5 Platform condition	Satisfactory
2.6 Sheaves & pins	Satisfactory
2.7 Mounting bolts	Satisfactory
2.8 Tyres / Crawler	Satisfactory
2.9 Markings of operation controls	Satisfactory
2.10 Outriggers / Stabilizers	Not applicable
3. HYDRAULIC SYSTEM	
3.1 Cylinder	Satisfactory
3.2 Motors/ Power Train	Satisfactory
3.3 Hydraulic Pump	Satisfactory
3.4 Tank & oil	Satisfactory
3.5 Hoses	Satisfactory
3.6 Steering system	Satisfactory
4. POWER UNIT	
4.1 Engine	Satisfactory
4.2 Spark arrestor	Satisfactory
4.3 Operator control panel	Satisfactory
4.4 Gear boxes	Satisfactory
5. SLEW UNIT	
5.1 Rack & pinion	Satisfactory

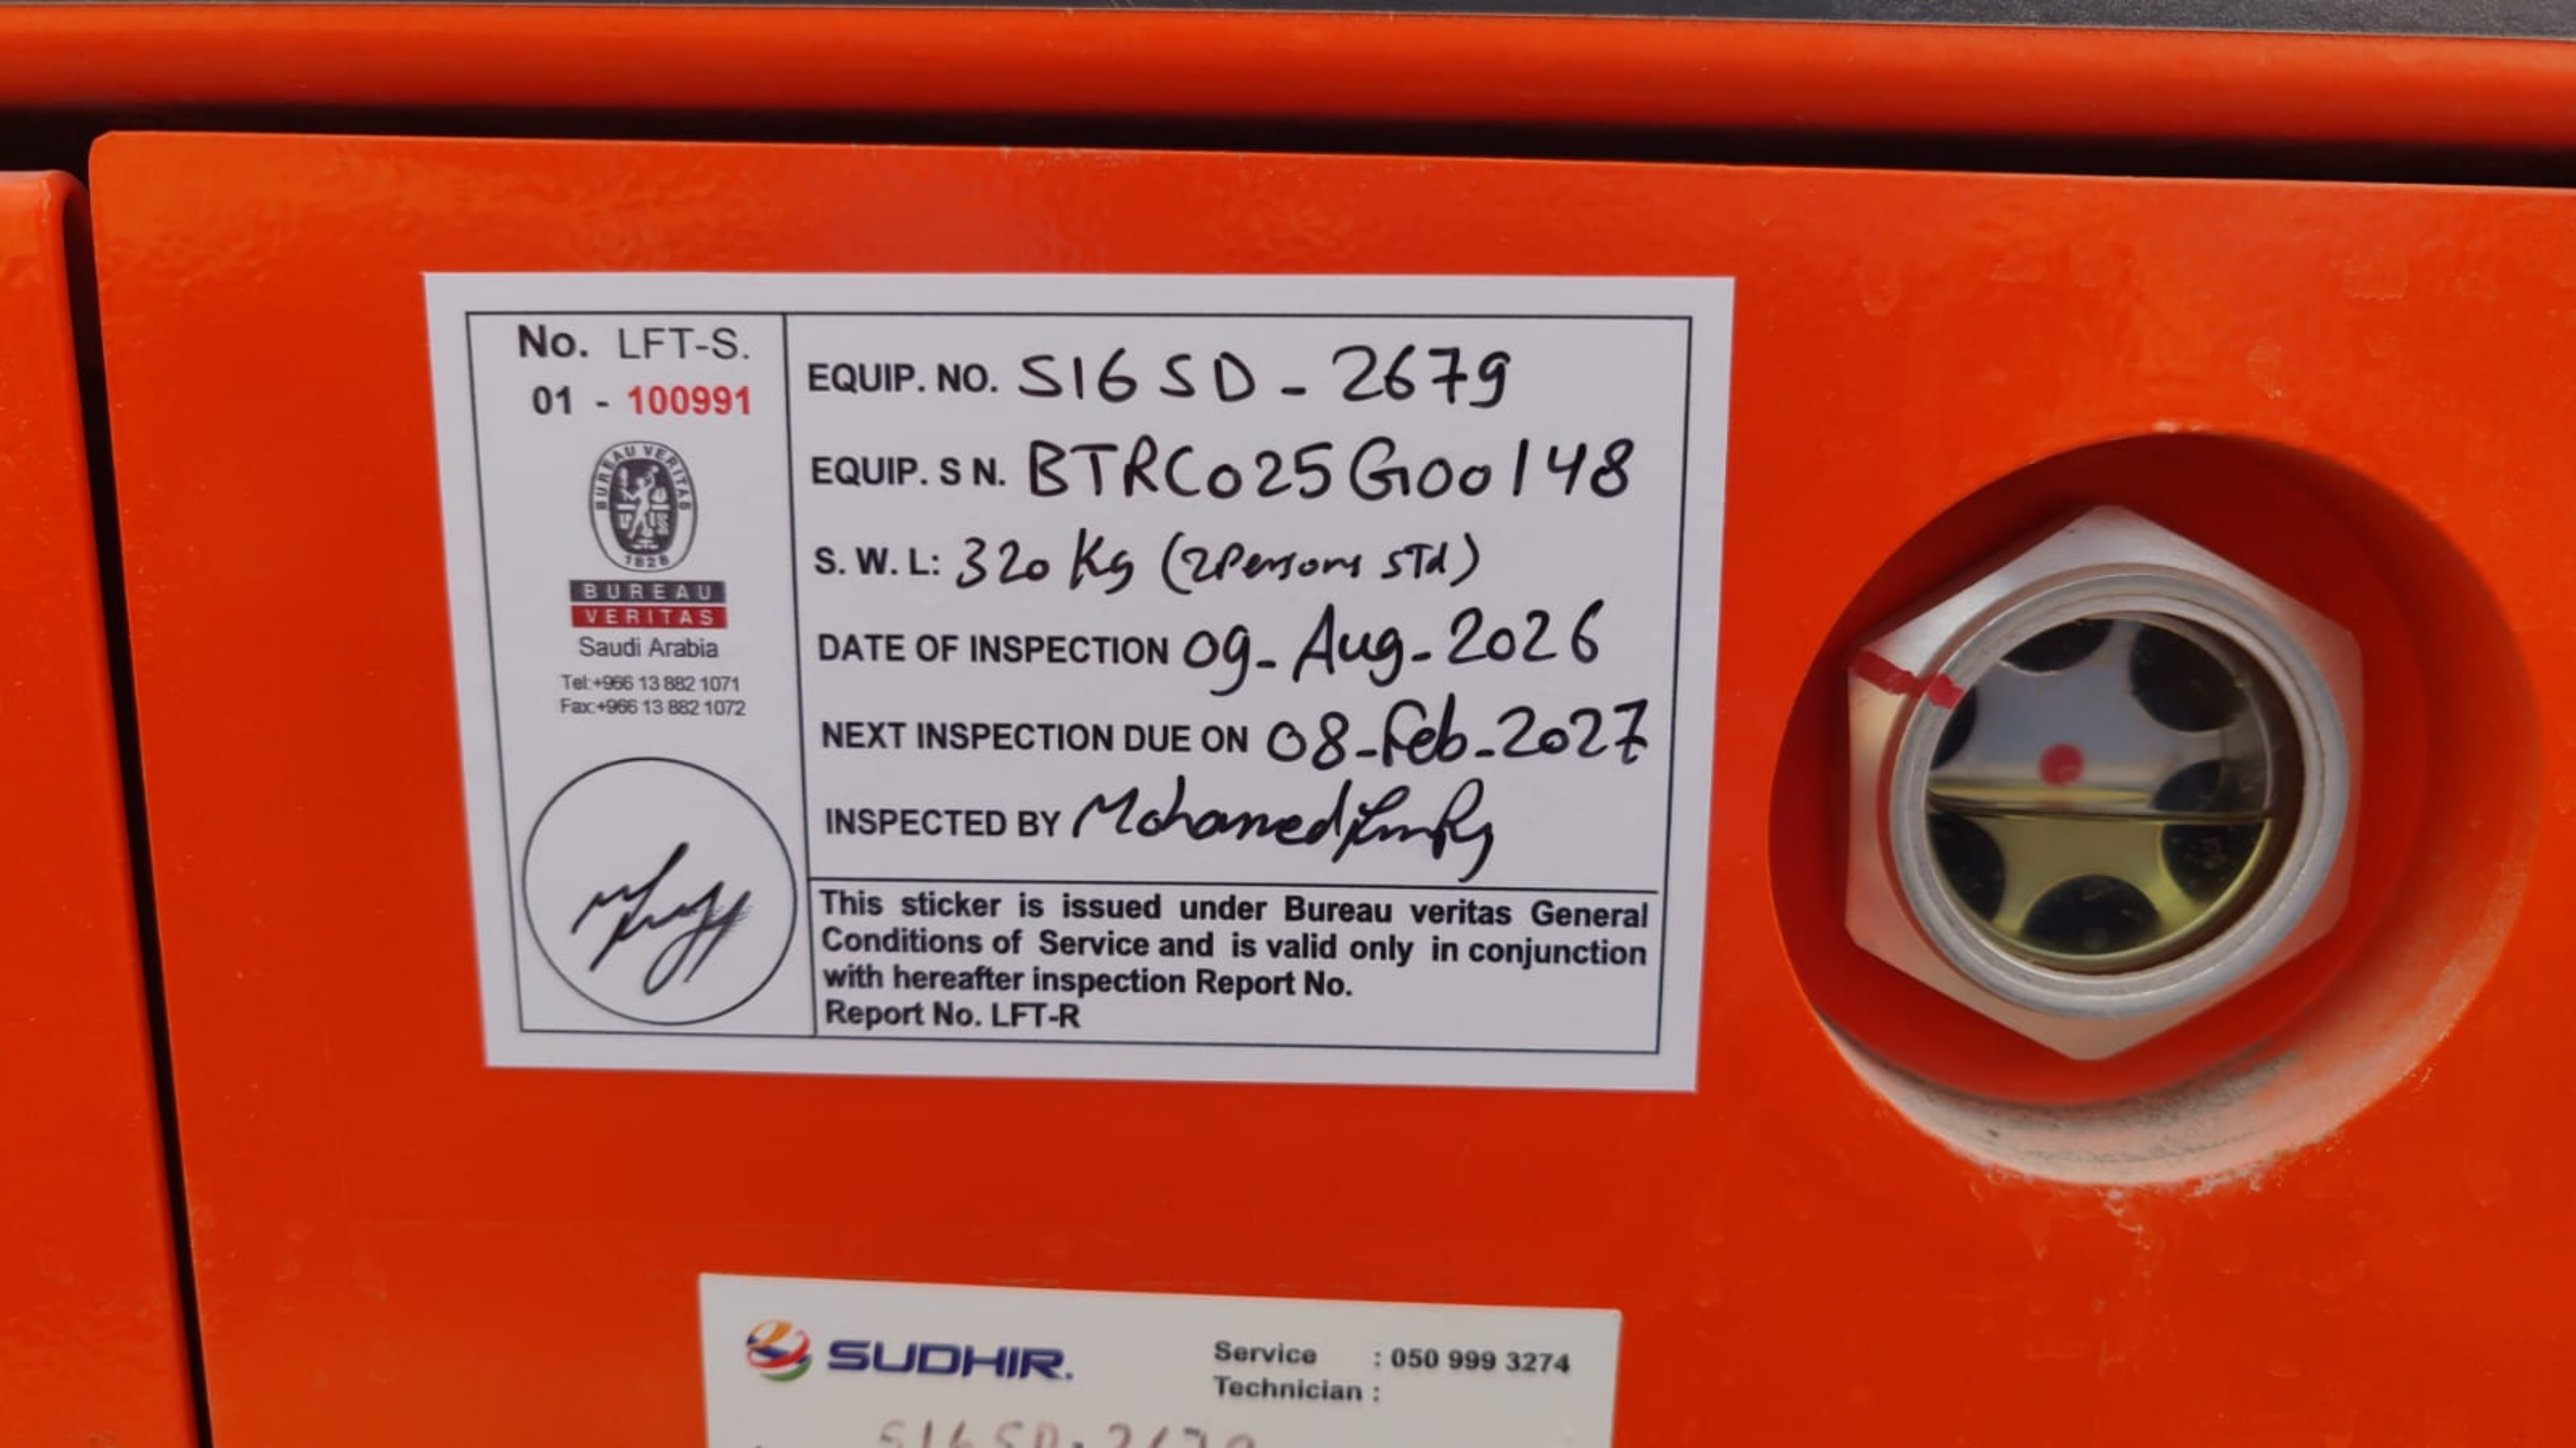
5.2 Bearings	Satisfactory
5.3 Bearing bolts	Satisfactory
5.4 Brakes	Satisfactory
5.5 Swing lock	Satisfactory
6.SAFETY DEVICE	
6.1 Motion Alarm	Satisfactory
6.2 Auxiliary Power Unit (Emergency Lowering system)	Satisfactory
6.3 Overload protection	Satisfactory
6.4 Limit switches	Satisfactory
6.5 Speed control	Satisfactory
6.6 Emergency stop	Satisfactory
6.7 Fire Extinguisher	Satisfactory
6.8 Tilt Buzzer	Satisfactory
6.9 Rotating warning light	Satisfactory
6.10 Working hours meter	Satisfactory

Inspector to Bureau Veritas
Signature:





Name: Mohamed Elsabry
Position: Inspector


No. LFT-S.
01 - 100991
BUREAU VERITAS
Saudi Arabia
Tel:+966 13 882 1071
Fax:+966 13 882 1072
EQUIP. NO. S16 SD - 2679
EQUIP. S N. BTRC025G00148
S. W. L: 320 Kg (2Persons STd)
DATE OF INSPECTION 09-Aug-2026
NEXT INSPECTION DUE ON 08-Feb-2027
INSPECTED BY Mohamed Lutfy
This sticker is issued under Bureau veritas General Conditions of Service and is valid only in conjunction with hereafter inspection Report No.
Report No. LFT-R
SUDHIR.
Service : 050 999 3274
Technician :
